

Assembly #24 - Window
1747 x 2350 x 30 (1)


Miscellaneous

2	Window Frame	Black



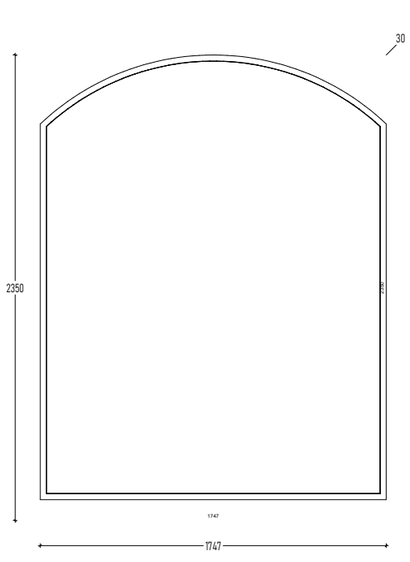



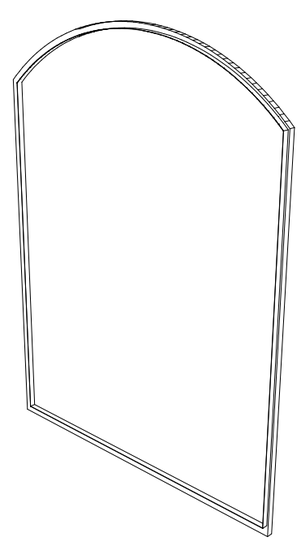

Top Reveal = 3

LHS Reveal = 2 RHS Reveal = 2

Bot Reveal = 0

Hor Reveal = 2

Vert Reveal = 2

J936 - Barry St Basement


Wine Cellar) - Wall #1


Date: 15/10/26


Assembly #25 - Window
1747 x 2350 x 30 (1)

Miscellaneous

2	Window Frame	Black

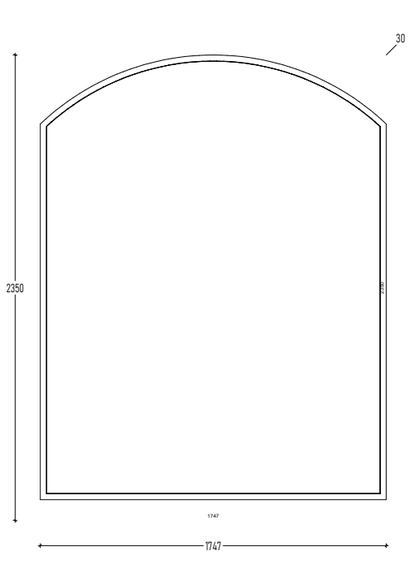



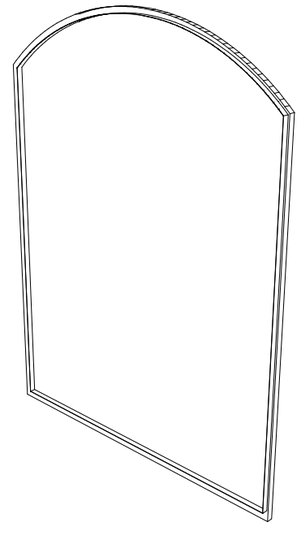

Top Reveal = 3

LHS Reveal = 2 RHS Reveal = 2

Bot Reveal = 0

Hor Reveal = 2

Vert Reveal = 2

J936 - Barry St Basement


Wine Cellar) - Wall #2


Date: 15/10/26


Assembly #26 - Window
1747 x 2350 x 30 (1)

Miscellaneous

2	Window Frame	Black

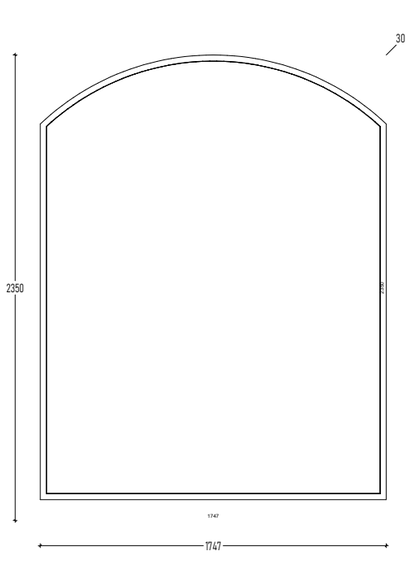



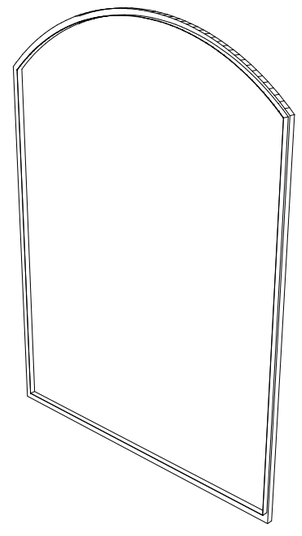

Top Reveal = 3

LHS Reveal = 2 RHS Reveal = 2

Bot Reveal = 0

Hor Reveal = 2

Vert Reveal = 2

J936 - Barry St Basement


Wine Cellar) - Wall #3


Date: 15/10/26

Assembly #27 - Window
1746 x 2350 x 30 (1)


Miscellaneous

2	Window Frame	Black

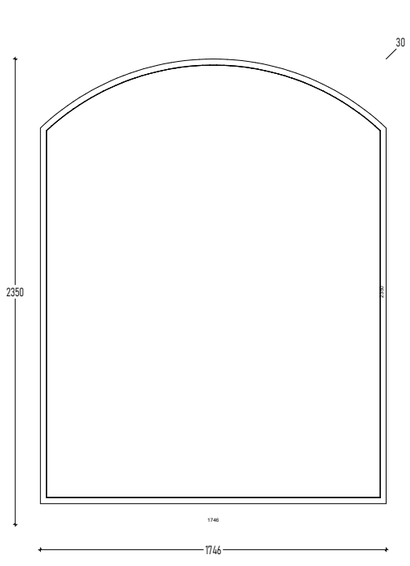





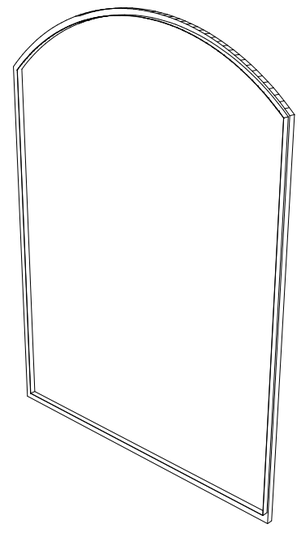

Top Reveal = 3

LHS Reveal = 2 RHS Reveal = 2

Bot Reveal = 0

Hor Reveal = 2

Vert Reveal = 2

J936 - Barry St Basement


Wine Cellar) - Wall #4


Date: 15/10/26


Assembly #28 - Toe Assembly
484 x 50 x 330 (1)

Parts Within Cabinet


2	50	247	Sleeper	16mm Packing Sheet
2	50	247	Top Sleeper	16mm Packing Sheet
1	50	444	Front Toe	16mm Packing Sheet
1	484	70	Front Kick Face	19mm American Oak G2S
1	50	444	Back Toe	16mm Packing Sheet



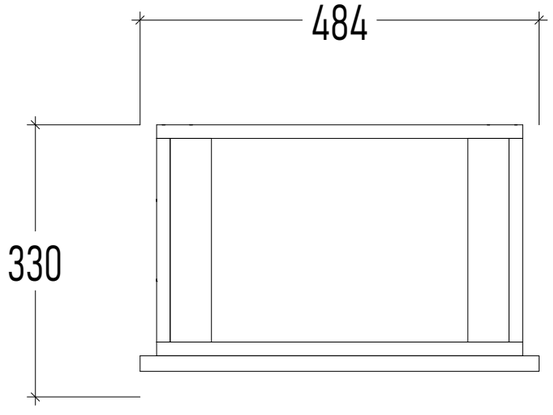

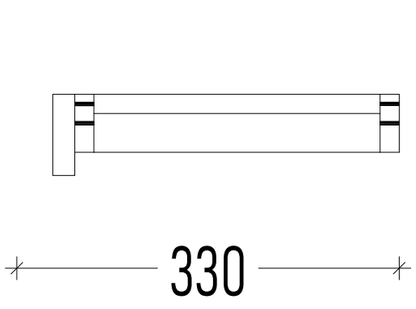

50

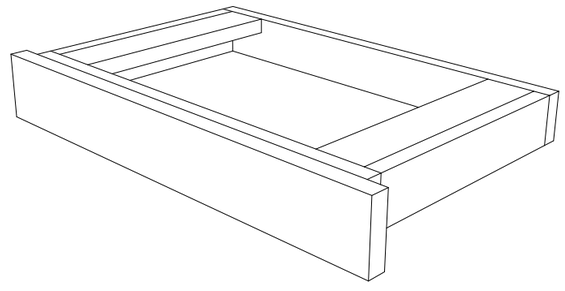

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J936 - Barry St Basement


Wine Cellar) - Wall #5

Date: 15/10/26

Assembly #29 - Tall Filler to Kick
20 x 1715 x 420 (1)

Parts Within Cabinet

1	60	1715	Filler	19mm American Oak G2S

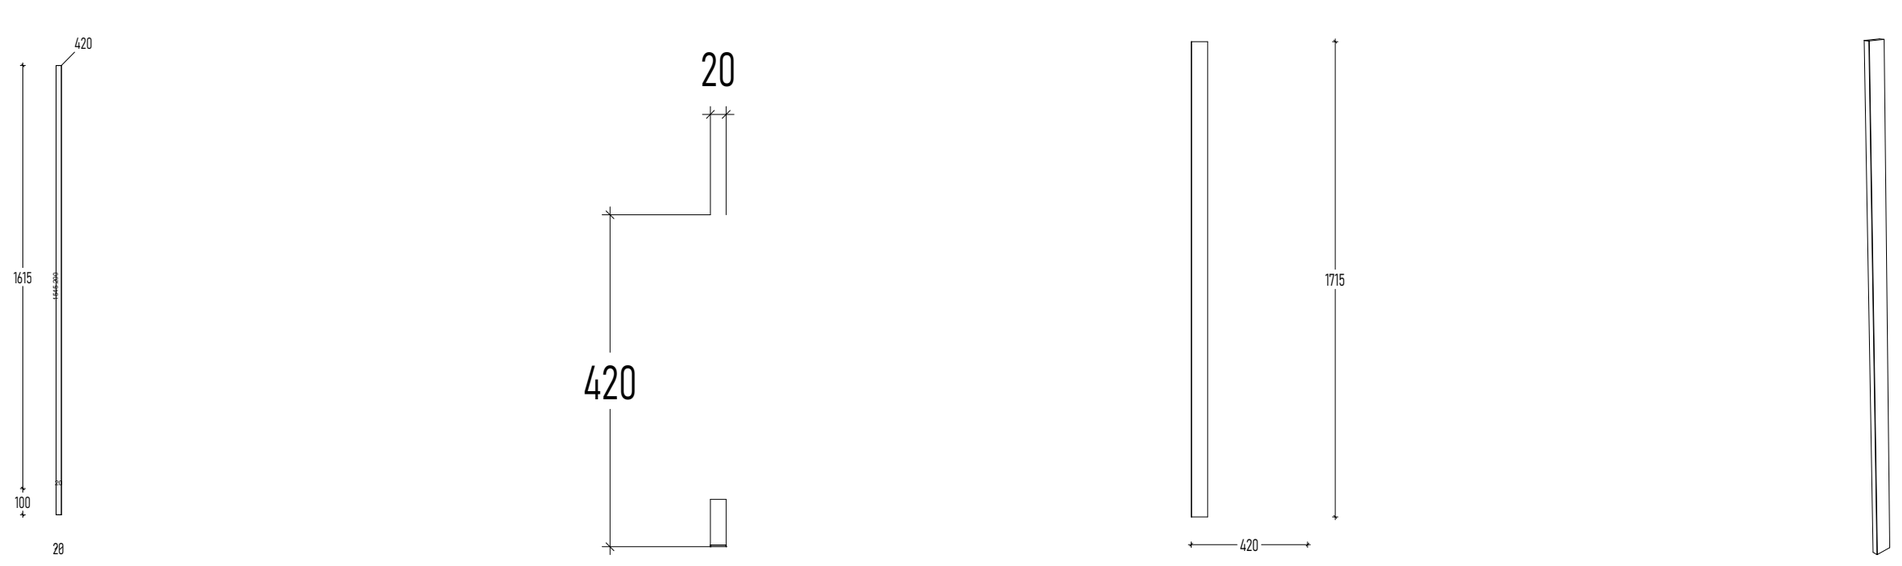

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J936 - Barry St Basement

Wine Cellar) - Wall #5

Date: 15/10/26


Assembly #30 - Std Tall Wine Rack
444 x 1715 x 330 (1)


Parts Within Cabinet


1	311	1677	Left End	19mm American Oak G2S
1	311	1677	Right End	19mm American Oak G2S
1	444	1677	Unfinished Back	19mm American Oak G2S
1	330	444	Top	19mm American Oak G2S
1	330	444	Bottom	19mm American Oak G2S
1	404	391	Internal Removable Back	19mm American Oak G2S
1	311	406	Shelf	19mm American Oak G2S
3	311	1265	Partition	19mm American Oak G2S
11	311	405	Fixed Shelf	19mm American Oak G2S


Miscellaneous

11	Plant	System Plant



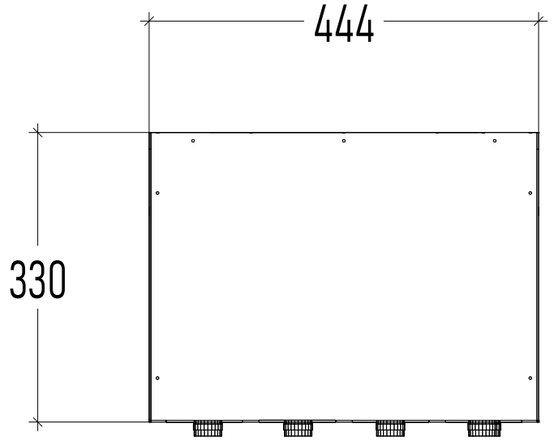





Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J936 - Barry St Basement


Wine Cellar) - Wall #5


Date: 15/10/26


Assembly #31 - Tall Filler to Kick
20 x 1715 x 420 (1)

Parts Within Cabinet

1	60	1715	Filler	19mm American Oak G2S









Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

J936 - Barry St Basement

Hor Reveal = 0


Vert Reveal = 2


Wine Cellar) - Wall #5


Date: 15/10/26


Assembly #32 - Empty Upper Object
484 x 615 x 446 (1)

Miscellaneous
1 Brick Gray

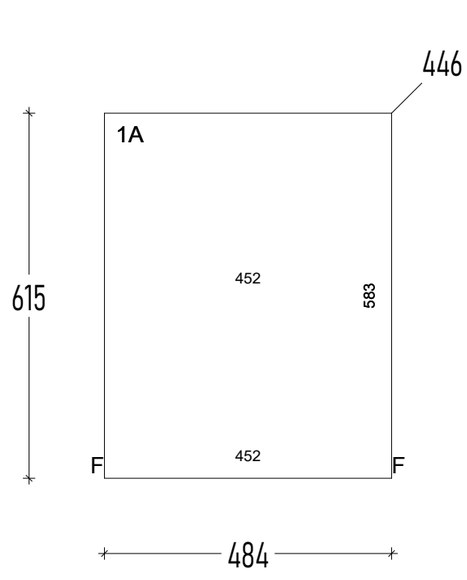

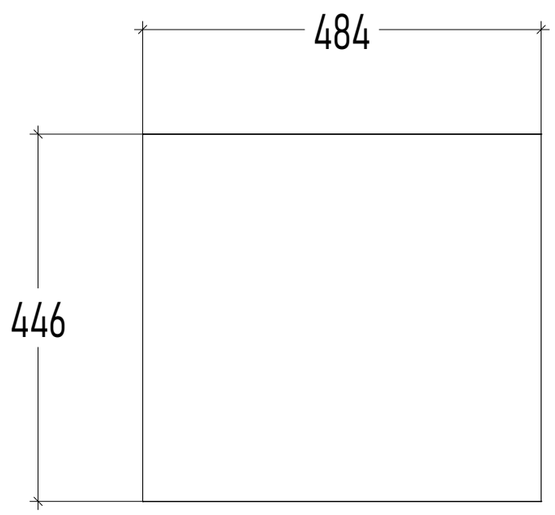

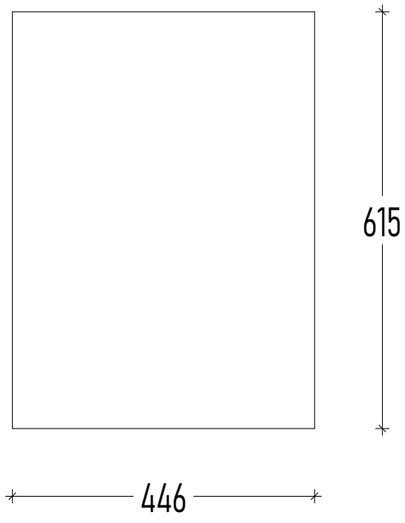

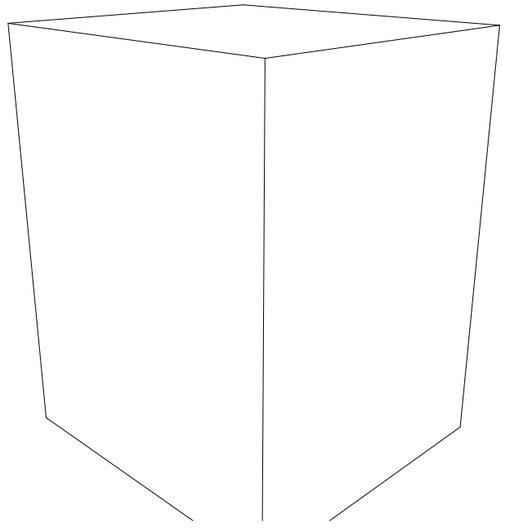

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

J936 - Barry St Basement

Hor Reveal = 0

Vert Reveal = 2


Wine Cellar) - Wall #5


Date: 15/10/26

Assembly #33 - Top Shadowline
484 x 20 x 420 (1)


Parts Within Cabinet

1	60	484	Top Shadow	18mm Satin MDF



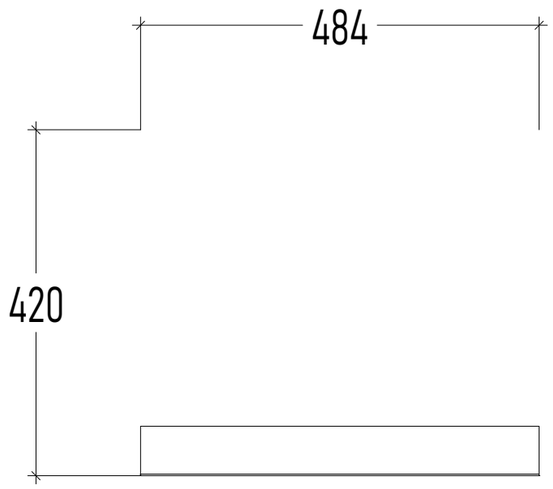



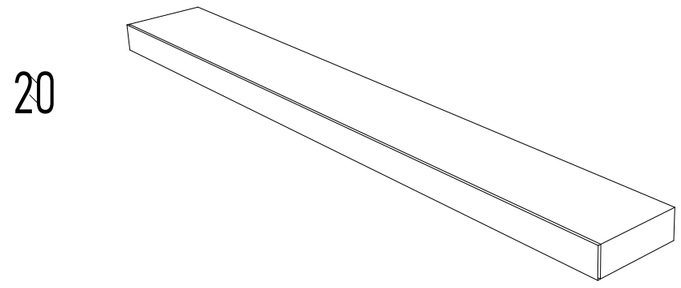

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J936 - Barry St Basement


Wine Cellar) - Wall #5


Date: 15/10/26


Assembly #34 - Toe Assembly
487 x 50 x 330 (1)

Parts Within Cabinet


2	50	247	Sleeper	16mm Packing Sheet
2	50	247	Top Sleeper	16mm Packing Sheet
1	50	447	Front Toe	16mm Packing Sheet
1	487	70	Front Kick Face	19mm American Oak G2S
1	50	447	Back Toe	16mm Packing Sheet



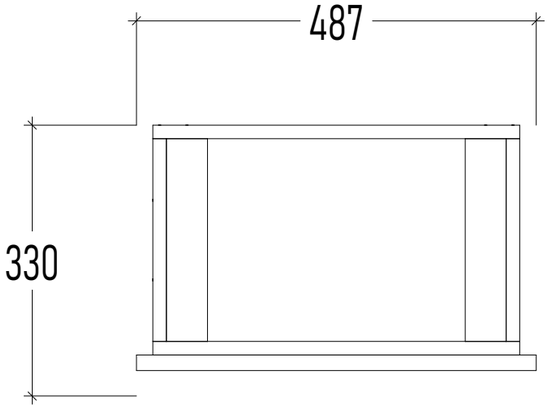

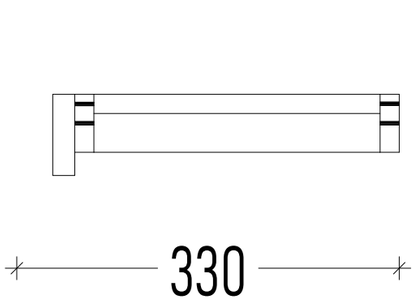



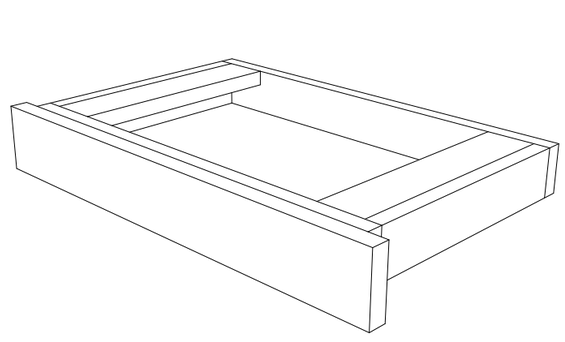

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

J936 - Barry St Basement

Hor Reveal = 0

Vert Reveal = 2


Wine Cellar) - Wall #6


Date: 15/10/26


Assembly #35 - Tall Filler to Kick
20 x 1715 x 420 (1)

Parts Within Cabinet

1	60	1715	Filler	19mm American Oak G2S









Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J936 - Barry St Basement

Wine Cellar) - Wall #6

Date: 15/10/26


Assembly #36 - Std Tall Wine Rack
447 x 1715 x 330 (1)


Parts Within Cabinet


1	311	1677	Left End	19mm American Oak G2S
1	311	1677	Right End	19mm American Oak G2S
1	447	1677	Unfinished Back	19mm American Oak G2S
1	330	447	Top	19mm American Oak G2S
1	330	447	Bottom	19mm American Oak G2S
1	404	391	Internal Removable Back	19mm American Oak G2S
1	311	409	Shelf	19mm American Oak G2S
3	311	1265	Partition	19mm American Oak G2S
11	311	408	Fixed Shelf	19mm American Oak G2S


Miscellaneous

11	Plant	System Plant



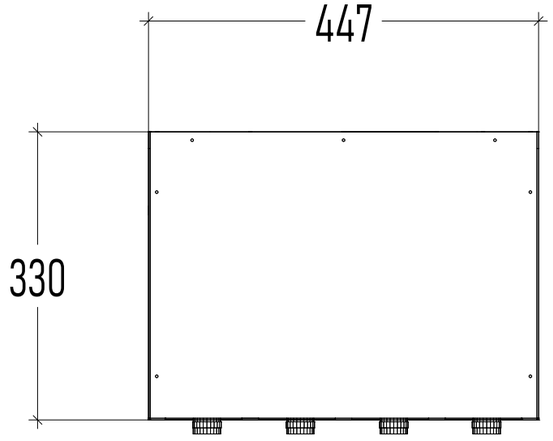





Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

J936 - Barry St Basement

Hor Reveal = 0

Vert Reveal = 2


Wine Cellar) - Wall #6


Date: 15/10/26


Assembly #37 - Tall Filler to Kick
20 x 1715 x 420 (1)

Parts Within Cabinet

1	60	1715	Filler	19mm American Oak G2S









Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

J936 - Barry St Basement

Hor Reveal = 0


Vert Reveal = 2


Wine Cellar) - Wall #6


Date: 15/10/26


Assembly #38 - Empty Upper Object
487 x 615 x 440 (1)

Miscellaneous
1 Brick Gray

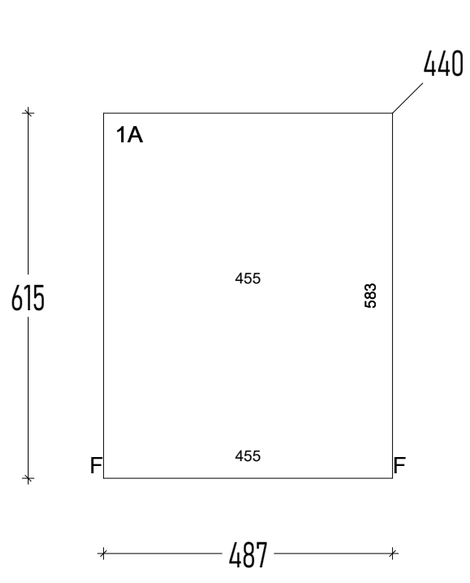

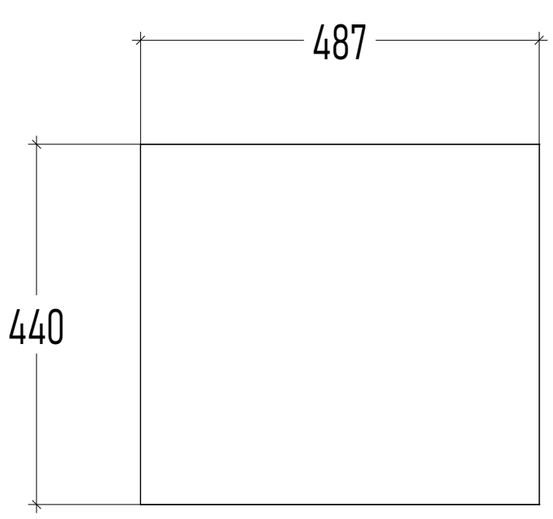

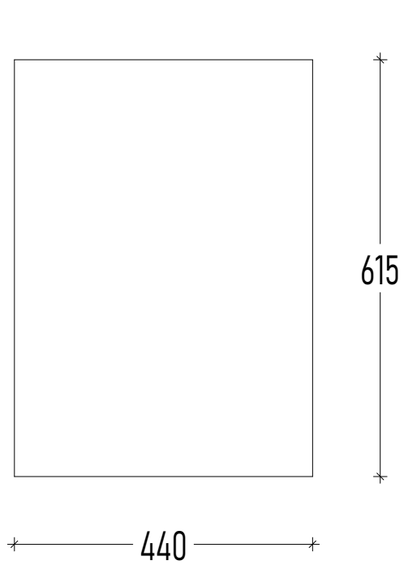

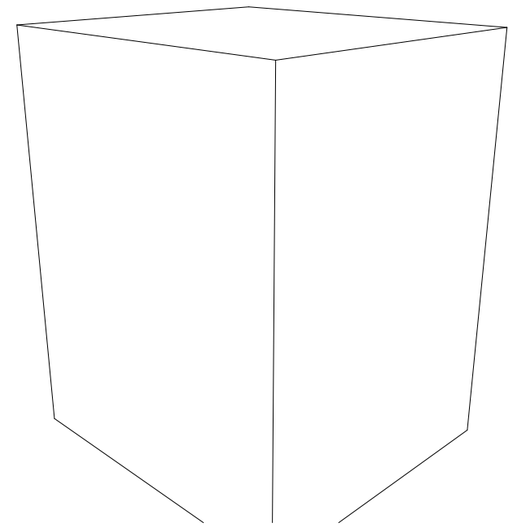

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

J936 - Barry St Basement

Hor Reveal = 0

Vert Reveal = 2


Wine Cellar) - Wall #6


Date: 15/10/26

Assembly #39 - Top Shadowline
487 x 20 x 420 (1)


Parts Within Cabinet

1	60	487	Top Shadow	18mm Satin MDF



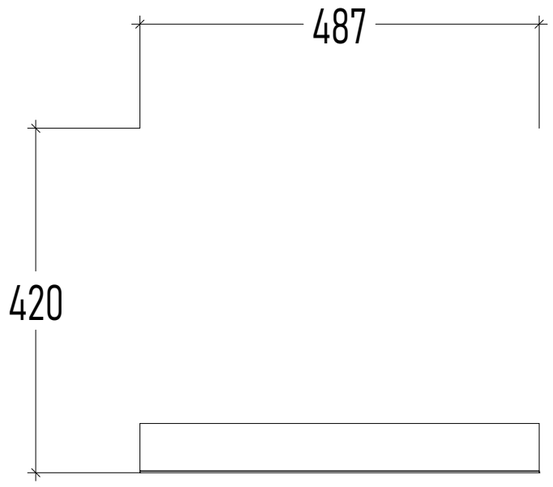



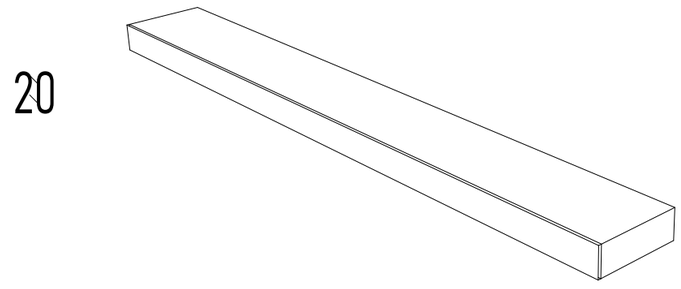

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J936 - Barry St Basement


Wine Cellar) - Wall #6


Date: 15/10/26


Assembly #40 - Window
1500 x 2350 x 30 (1)


Miscellaneous

3	Window Frame	Black

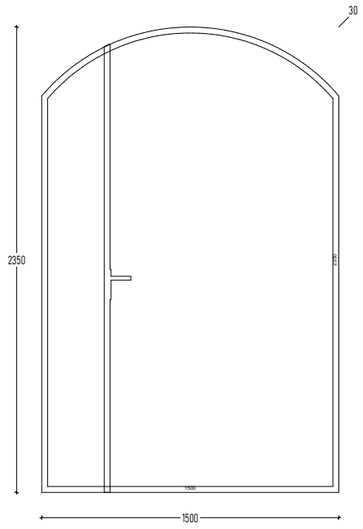





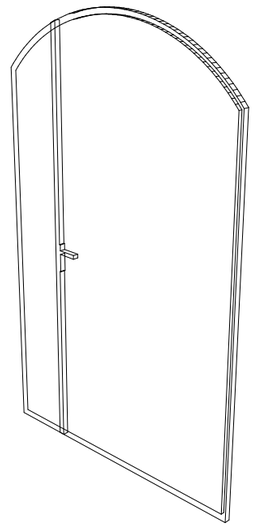

Top Reveal = 3

LHS Reveal = 2 RHS Reveal = 2

Bot Reveal = 0

Hor Reveal = 2

Vert Reveal = 2

J936 - Barry St Basement

Wine Cellar) - Wall #10

Date: 15/10/26

Assembly #100 - Std Base 1 Door
1745 x 2000 x 440 (1)

Parts Within Cabinet


1	400	733	100.1 Left End	33mm Grain	
1	400	733	100.1 Right End	33mm Grain	
1	400	1745	100.1 Top	33mm Grain	*** ADD 45 ON THE BACK EDGE AI
3	400	733	100.1 Partition	33mm Grain	
1	400	1678	100.1 Fixed Shelf	33mm Grain	
3	59	1745	8.2 Fixed Shelf Apron	19mm American Oak G2S	
3	385.197	1745	Angled Fixed Shelf	19mm American Oak G2S	
3	379.821	536	33mm Vertical Partition	33mm Grain	
4	30	1729	30 x 30 x 3 SHS	50mm Steel SHS	
4	6	240	6mm End Plate	50mm Steel SHS	
10	16	134	30 x 30 x 3 SHS	50mm Steel SHS	
1	602	1250	Side Shelf & LED Jigs	12mm Board	
1	100	1745	Mitred 50mm Edge Apron	33mm Grain	***EDGE 2 LONG AND 45 1 LONG A


Miscellaneous


6	100.2 Plant	System Plant
1	Bottom	20mm Stone
7	3mm Ali Sheet	Black
3	LED	Black

Hardware

32	Lamello Clamex	Lamello Clamex P14 - Movable 10

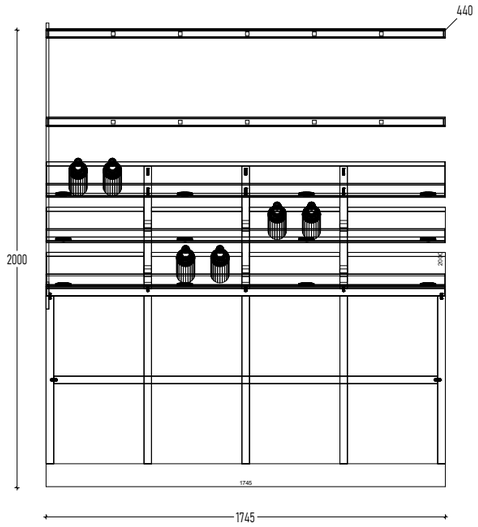

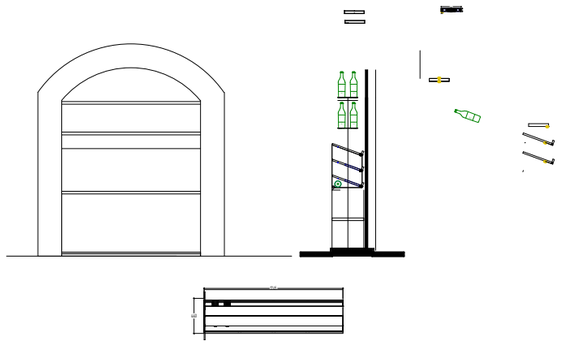





Top Reveal = 3

LHS Reveal = 2 RHS Reveal = 2

Bot Reveal = 0

Hor Reveal = 2

Vert Reveal = 2

J936 - Barry St Basement

Wine Cellar) - Wall #1

Date: 15/10/26

Assembly #200 - Std Base 1 Door
1745 x 2000 x 440 (1)

Parts Within Cabinet


1	400	733	200.1 Left End	33mm Grain	
1	400	733	200.1 Right End	33mm Grain	
1	400	1745	200.1 Top	33mm Grain	*** ADD 45 ON THE BACK EDGE AI
3	400	733	200.1 Partition	33mm Grain	
1	400	1678	200.1 Fixed Shelf	33mm Grain	
3	59	1745	8.2 Fixed Shelf Apron	19mm American Oak G2S	
3	385.197	1745	Angled Fixed Shelf	19mm American Oak G2S	
3	379.821	536	33mm Vertical Partition	33mm Grain	
4	30	1729	30 x 30 x 3 SHS	50mm Steel SHS	
4	6	240	6mm End Plate	50mm Steel SHS	
10	16	134	30 x 30 x 3 SHS	50mm Steel SHS	
1	100	1745	Mitred 50mm Edge Apron	33mm Grain	***EDGE 2 LONG AND 45 1 LONG A


Miscellaneous


6	200.2 Plant	System Plant
1	Bottom	20mm Stone
7	3mm Ali Sheet	Black
3	LED	Black

Hardware

32	Lamello Clamex	Lamello Clamex P14 - Movable 10

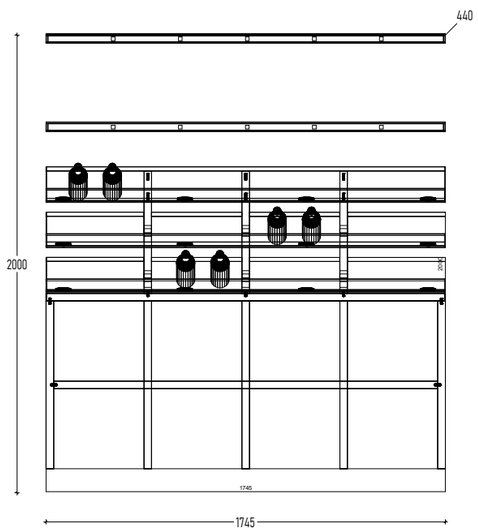

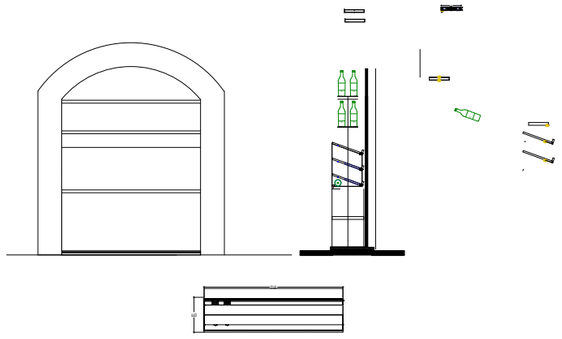





Top Reveal = 3

LHS Reveal = 2 RHS Reveal = 2

Bot Reveal = 0

Hor Reveal = 2

Vert Reveal = 2

J936 - Barry St Basement

Wine Cellar) - Wall #2

Date: 15/10/26

Assembly #300 - Std Base 1 Door
1745 x 2000 x 440 (1)

Parts Within Cabinet


1	400	733	300.1 Left End	33mm Grain	
1	400	733	300.1 Right End	33mm Grain	
1	400	1745	300.1 Top	33mm Grain	*** ADD 45 ON THE BACK EDGE AI
3	400	733	300.1 Partition	33mm Grain	
1	400	1678	300.1 Fixed Shelf	33mm Grain	
3	59	1745	8.2 Fixed Shelf Apron	19mm American Oak G2S	
3	385.197	1745	Angled Fixed Shelf	19mm American Oak G2S	
3	379.821	536	33mm Vertical Partition	33mm Grain	
4	30	1729	30 x 30 x 3 SHS	50mm Steel SHS	
4	6	240	6mm End Plate	50mm Steel SHS	
10	16	134	30 x 30 x 3 SHS	50mm Steel SHS	
1	100	1745	Mitred 50mm Edge Apron	33mm Grain	***EDGE 2 LONG AND 45 1 LONG A


Miscellaneous


6	300.2 Plant	System Plant
1	Bottom	20mm Stone
7	3mm Ali Sheet	Black
3	LED	Black

Hardware

32	Lamello Clamex	Lamello Clamex P14 - Movable 10

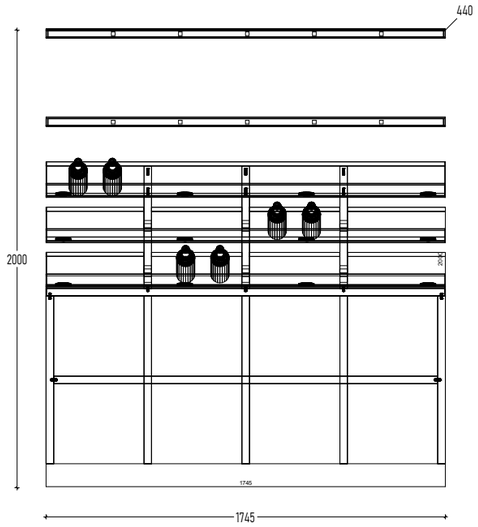

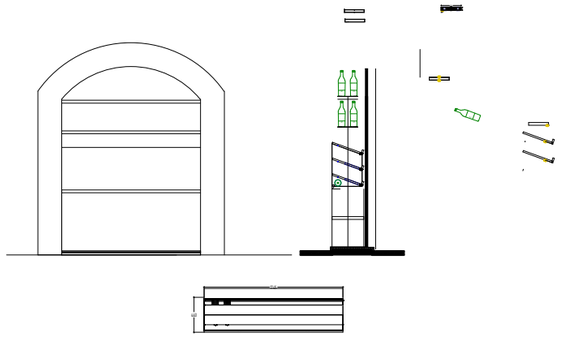





Top Reveal = 3

LHS Reveal = 2 RHS Reveal = 2

Bot Reveal = 0

Hor Reveal = 2

Vert Reveal = 2

J936 - Barry St Basement

Wine Cellar) - Wall #3

Date: 15/10/26

Assembly #400 - Std Base 1 Door
1745 x 2000 x 440 (1)

Parts Within Cabinet


1	400	733	400.1 Left End	33mm Grain	
1	400	733	400.1 Right End	33mm Grain	
1	400	1745	400.1 Top	33mm Grain	*** ADD 45 ON THE BACK EDGE AI
3	400	733	400.1 Partition	33mm Grain	
1	400	1678	400.1 Fixed Shelf	33mm Grain	
3	59	1745	8.2 Fixed Shelf Apron	19mm American Oak G2S	
3	385.197	1745	Angled Fixed Shelf	19mm American Oak G2S	
3	379.821	536	33mm Vertical Partition	33mm Grain	
4	30	1729	30 x 30 x 3 SHS	50mm Steel SHS	
4	6	240	6mm End Plate	50mm Steel SHS	
10	16	134	30 x 30 x 3 SHS	50mm Steel SHS	
1	100	1745	Mitred 50mm Edge Apron	33mm Grain	***EDGE 2 LONG AND 45 1 LONG A


Miscellaneous


6	400.2 Plant	System Plant
1	Bottom	20mm Stone
7	3mm Ali Sheet	Black
3	LED	Black

Hardware

32	Lamello Clamex	Lamello Clamex P14 - Movable 10

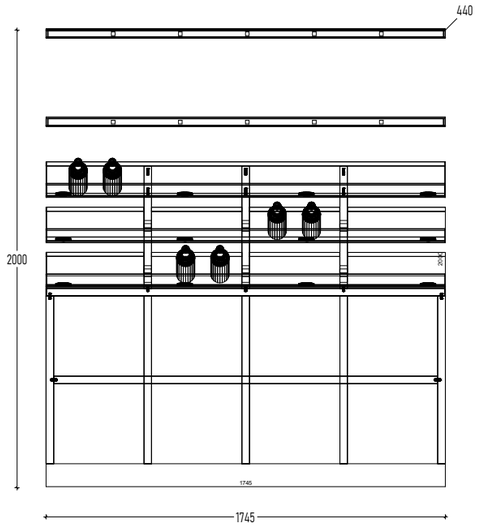

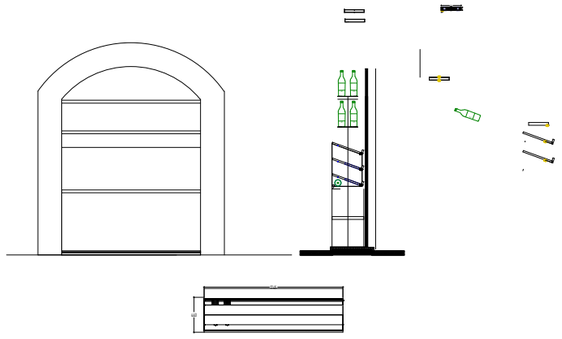





Top Reveal = 3

LHS Reveal = 2 RHS Reveal = 2

Bot Reveal = 0

Hor Reveal = 2

Vert Reveal = 2

J936 - Barry St Basement

Wine Cellar) - Wall #4

Date: 15/10/26
