

Assembly #17 - Toe Assembly
2482 x 100 x 580 (1)


Parts Within Cabinet

6	80	497	Sleeper	16mm Packing Sheet
6	80	497	Top Sleeper	16mm Packing Sheet
1	100	2482	Front Toe	16mm Packing Sheet
1	2482	120	Front Kick Face	18mm Polytec Florentine Walnut Woodma.
1	100	2482	Back Toe	16mm Packing Sheet









Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 2

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen


Bed 1 Robe) - Wall #4


Date: 28/09/26


Assembly #18 - Tall Panel to Floor
18 x 2960 x 600 (1)


Parts Within Cabinet

1	620	2980	Panel	18mm Polytec Florentine Walnut Woodma









Top Reveal = 0

LHS Reveal = 2 RHS Reveal = 0

Bot Reveal = 0

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Hor Reveal = 0

Vert Reveal = 2

Bed 1 Robe) - Wall #4

Date: 28/09/26

Assembly #19 - C BASE 4 DRAWER
814 x 884 x 580 (1)

Drawer Fronts

1	811	183	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	
3	811	210	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	852	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	852	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	814	852	Unfinished Back	16mm HMR White	
1	542	814	Top	16mm HMR White	
1	580	814	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	747	540	Drawer Box Bottom 1	16mm HMR White	
1	101	744	Drawer Box Back 1	16mm HMR White	
1	747	540	Drawer Box Bottom 2	16mm HMR White	
1	148	744	Drawer Box Back 2	16mm HMR White	
1	747	540	Drawer Box Bottom 3	16mm HMR White	
1	148	744	Drawer Box Back 3	16mm HMR White	
1	747	540	Drawer Box Bottom 4	16mm HMR White	
1	148	744	Drawer Box Back 4	16mm HMR White	

Drawers

1	P	LBox Wte Bmn 70 Kx550
3	P	LBox Wte Bmn 70 Cx550

Handles


4	240 overall - 192mm C - Brave - Metallic Brown


Miscellaneous


8	Legrabox Bmn 70kg	LBox DG Bmn 70Kg 550
2	Legrabox Drw Side	LBox Side Wte K 550
2	Legrabox Front Brkt	LBox Fnt Brkt K Exp
2	Legrabox Back Brkt	LBox Back Brkt Wte K
6	Legrabox Drw Side	LBox Side Wte C 550
12	Legrabox Front Brkt	LBox Fnt Brkt M Exp
6	Legrabox Back Brkt	LBox Back Brkt Wte C

Hardware

4	Drawer Pull	240 overall - 192mm C - Brave	240
4	Drawer Box Base Bracket	Blum Drawer Base Support	20
1 P	Drawer Guide	LBox Wte Bmn 70 Kx550	550
3 P	Drawer Guide	LBox Wte Bmn 70 Cx550	550

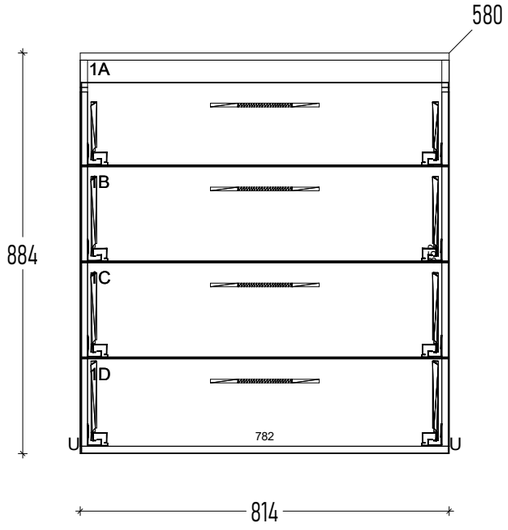

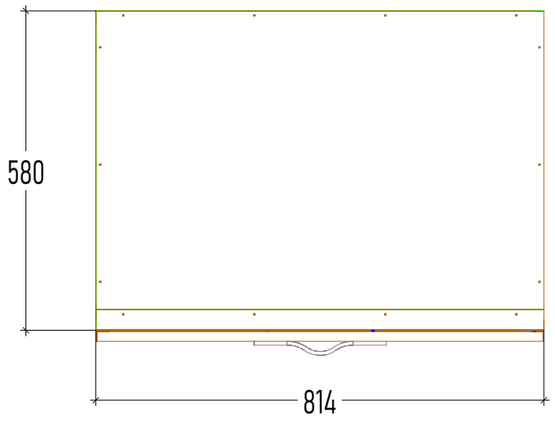

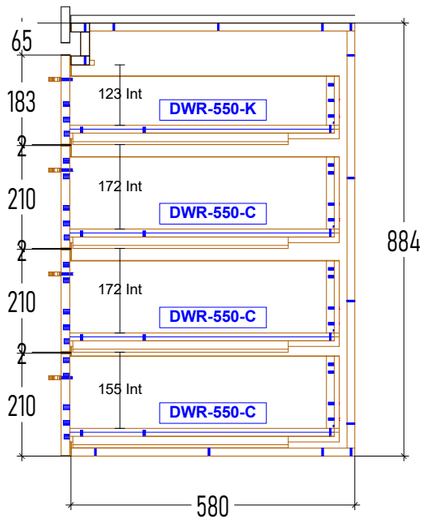



Top Reveal = 65

LHS Reveal = 2 RHS Reveal = 1

Bot Reveal = 0

Hor Reveal = 2

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen


Bed 1 Robe) - Wall #4


Date: 28/09/26


Assembly #19.1 - C WALL OPEN
814 x 85 x 38 (1)


Parts Within Cabinet

1	814	49	C Shape Fingerpull Rail	18mm Polytec Florentine Walnut Woodma*** MAKE INTO C SHAPE FINGERF
1	38	814	C Shape Fingerpull Top	18mm Polytec Florentine Walnut Woodma*** MAKE INTO C SHAPE FINGERF
1	38	814	C Shape Fingerpull Bottom	18mm Polytec Florentine Walnut Woodma*** MAKE INTO C SHAPE FINGERF





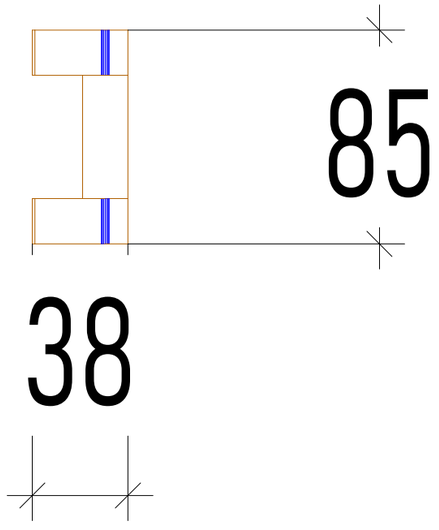

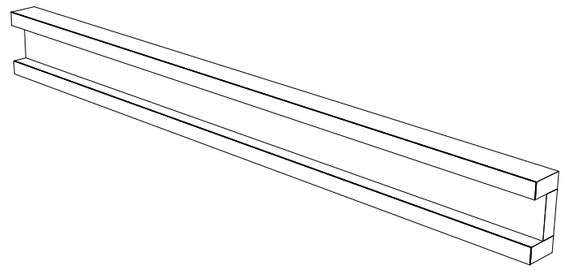

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 1 Robe) - Wall #4

Date: 28/09/26

Assembly #20 - C BASE 4 DRAWER
814 x 884 x 580 (1)

Drawer Fronts

1	812	183	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	
3	812	210	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	852	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	852	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	814	852	Unfinished Back	16mm HMR White	
1	542	814	Top	16mm HMR White	
1	580	814	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	747	540	Drawer Box Bottom 1	16mm HMR White	
1	101	744	Drawer Box Back 1	16mm HMR White	
1	747	540	Drawer Box Bottom 2	16mm HMR White	
1	148	744	Drawer Box Back 2	16mm HMR White	
1	747	540	Drawer Box Bottom 3	16mm HMR White	
1	148	744	Drawer Box Back 3	16mm HMR White	
1	747	540	Drawer Box Bottom 4	16mm HMR White	
1	148	744	Drawer Box Back 4	16mm HMR White	

Drawers

1	P	LBox Wte Bmn 70 Kx550
3	P	LBox Wte Bmn 70 Cx550

Handles


4	240 overall - 192mm C - Brave - Metallic Brown


Miscellaneous


8	Legrabox Bmn 70kg	LBox DG Bmn 70Kg 550
2	Legrabox Drw Side	LBox Side Wte K 550
2	Legrabox Front Brkt	LBox Fnt Brkt K Exp
2	Legrabox Back Brkt	LBox Back Brkt Wte K
6	Legrabox Drw Side	LBox Side Wte C 550
12	Legrabox Front Brkt	LBox Fnt Brkt M Exp
6	Legrabox Back Brkt	LBox Back Brkt Wte C

Hardware

4	Drawer Pull	240 overall - 192mm C - Brave	240
4	Drawer Box Base Bracket	Blum Drawer Base Support	20
1 P	Drawer Guide	LBox Wte Bmn 70 Kx550	550
3 P	Drawer Guide	LBox Wte Bmn 70 Cx550	550

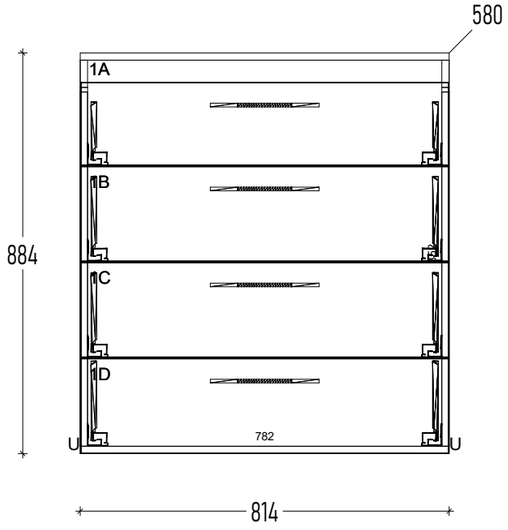

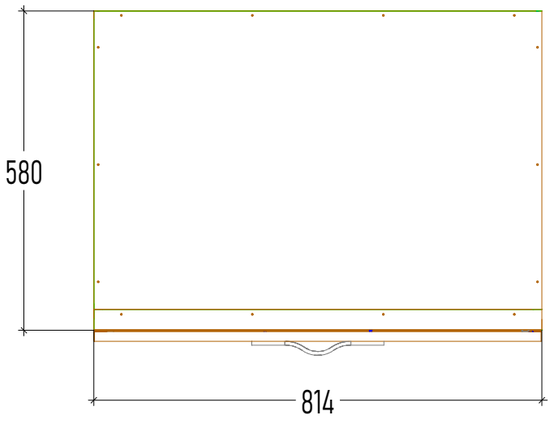

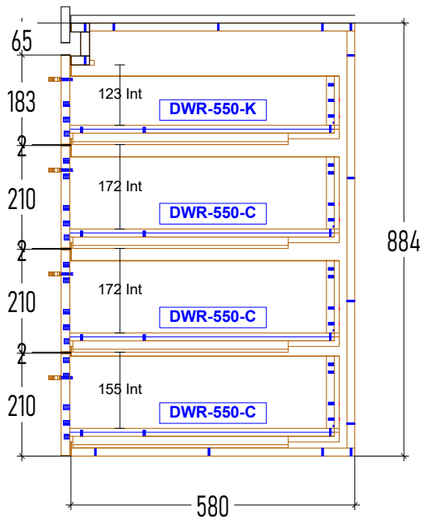



Top Reveal = 65

LHS Reveal = 1 RHS Reveal = 1

Bot Reveal = 0

Hor Reveal = 2

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen


Bed 1 Robe) - Wall #4


Date: 28/09/26


Assembly #20.1 - C WALL OPEN
814 x 85 x 38 (1)


Parts Within Cabinet

1	814	49	C Shape Fingerpull Rail	18mm Polytec Florentine Walnut Woodma*** MAKE INTO C SHAPE FINGERF
1	38	814	C Shape Fingerpull Top	18mm Polytec Florentine Walnut Woodma*** MAKE INTO C SHAPE FINGERF
1	38	814	C Shape Fingerpull Bottom	18mm Polytec Florentine Walnut Woodma*** MAKE INTO C SHAPE FINGERF





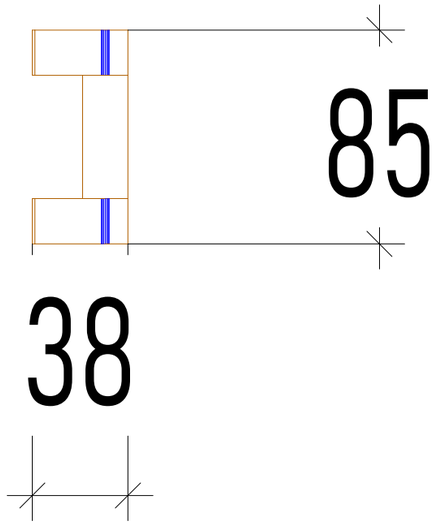

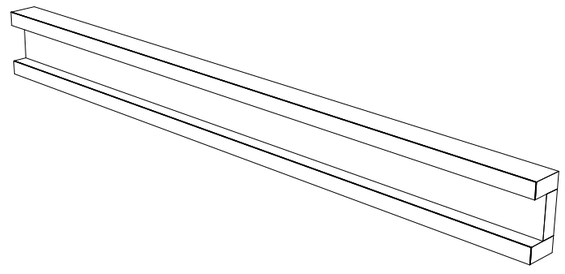

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 1 Robe) - Wall #4

Date: 28/09/26

Assembly #21 - Std Tall 1 Door
407 x 2050 x 580 (1)

Doors

1	406	2050	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	2018	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	2018	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	407	2018	Unfinished Back	16mm HMR White	
1	580	407	Top	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	580	407	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU

Handles

1	1040 OFFSET - 992mm C - Brave - Metallic Brown

Hinges

4	110 Deg Blum Hinge

Hinges Plates


4	Std Inline Hinge Plate


Miscellaneous


2	Rectangle Hanging Rail	Hanging Rail - Rectangular - Black	Cut to 365mm


Hardware

1	Door Pull	1040 OFFSET - 992mm C - Bra	1040
4	Hinge	110 Deg Blum Hinge	47
4	Hinge Plate	Std Inline Hinge Plate	19.5(



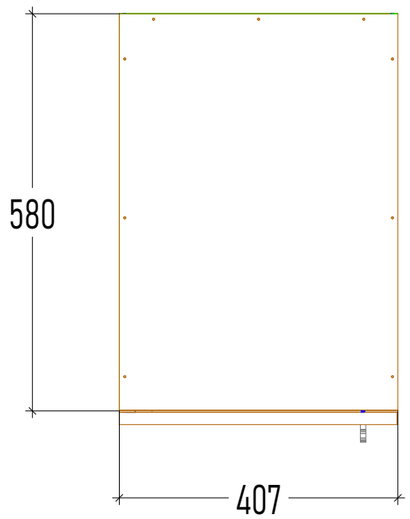





Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 1

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 1 Robe) - Wall #4

Date: 28/09/26

Assembly #22 - Std Tall 1 Door
407 x 2050 x 580 (1)

Doors

1	406	2050	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	2018	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	2018	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	407	2018	Unfinished Back	16mm HMR White	
1	580	407	Top	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	580	407	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU
2	554	373	Adjustable Shelf	16mm HMR White	

Handles

1	1040 OFFSET - 992mm C - Brave - Metallic Brown	

Hinges

4	110 Deg Blum Hinge	

Hinges Plates


4	Std Inline Hinge Plate	


Miscellaneous


1	Rectangle Hanging Rail	Hanging Rail - Rectangular - Black	Cut to 365mm


Hardware

1	Door Pull	1040 OFFSET - 992mm C - Bra	1040
4	Hinge	110 Deg Blum Hinge	47
4	Hinge Plate	Std Inline Hinge Plate	19.5(



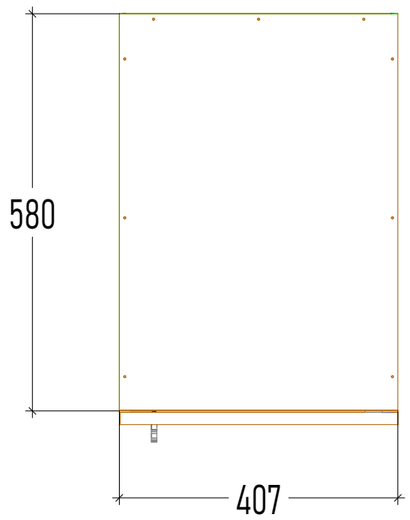





Top Reveal = 0

LHS Reveal = 1 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 1 Robe) - Wall #4


Date: 28/09/26


Assembly #23 - Tall Face Filler
40 x 2860 x 580 (1)

Parts Within Cabinet

1	60	2860	Filler	18mm Polytec Florentine Walnut Woodma	Cut width to 40mm









Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 2

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen


Bed 1 Robe) - Wall #4


Date: 28/09/26


Assembly #24 - BULKHEAD WALL OPEN
2482 x 40 x 580 (1)


Parts Within Cabinet

1	568	2420	Bulkhead Bottom	12mm Board	
1	580	40	Bulkhead Left End	12mm Board	45* 1 SHORT
1	2482	40	Bulkhead Face Panel	12mm Board	45* 1 SHORT







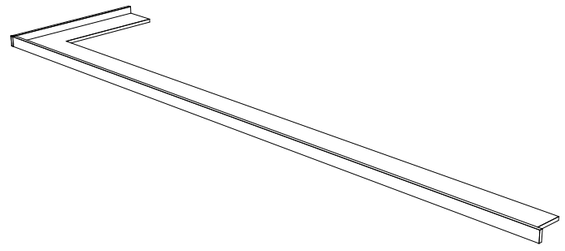

Top Reveal = 0

LHS Reveal = 2 RHS Reveal = 2

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 0

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 1 Robe) - Wall #4

Date: 28/09/26

Assembly #25 - STD WALL 2 DOOR
814 x 810 x 580 (1)

Doors

2	405.500	810	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	778	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	778	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	814	778	Unfinished Back	16mm HMR White	
1	580	814	Top	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	580	814	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	554	780	Adjustable Shelf	16mm HMR White	

Hinges


4 110 Deg Blum Hinge


Hinges Plates


4 Std Inline Hinge Plate


Hardware

4	Hinge	110 Deg Blum Hinge	47
4	Hinge Plate	Std Inline Hinge Plate	19.5(

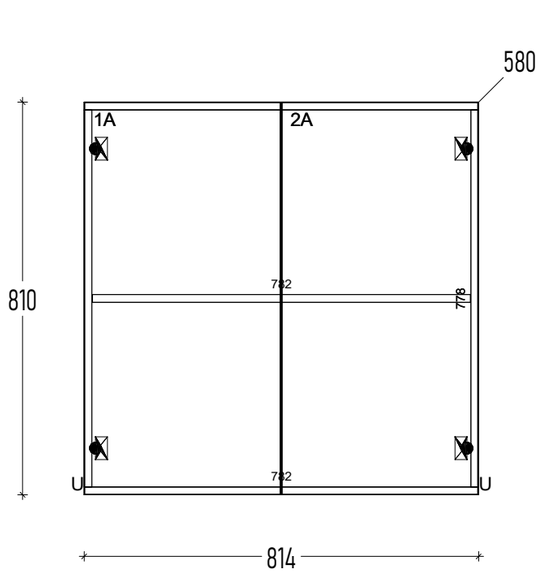

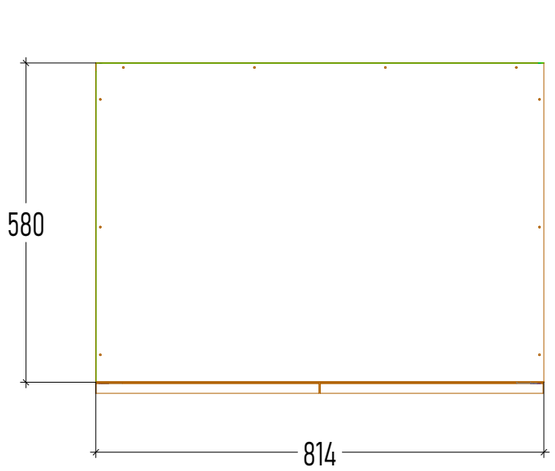

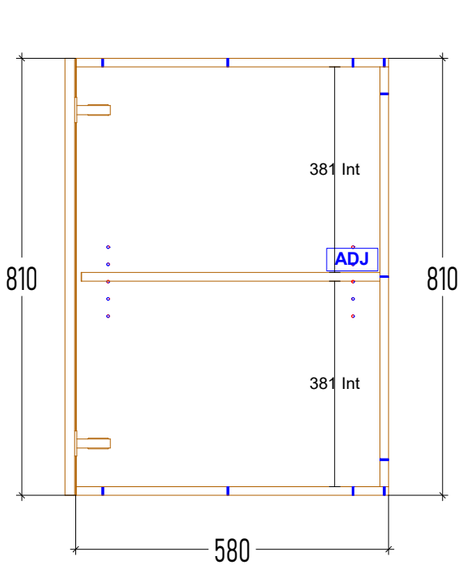

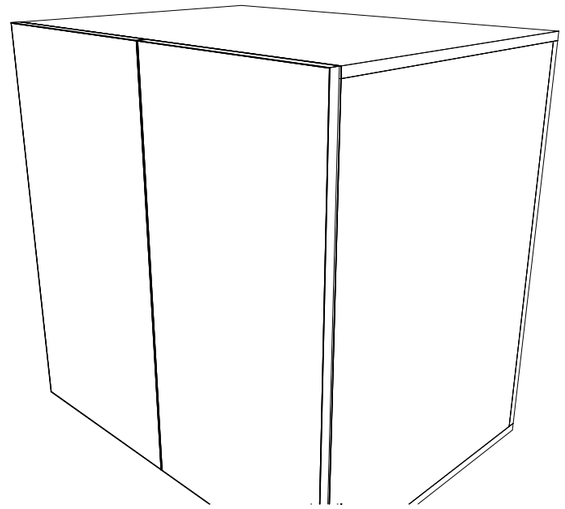

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 1

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 1 Robe) - Wall #4

Date: 28/09/26

Assembly #26 - STD WALL 2 DOOR
814 x 1166 x 580 (1)

Doors

2	405.500	1206	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	1134	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	1134	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	814	1134	Unfinished Back	16mm HMR White	
1	580	814	Top	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	580	814	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU

Hinges

6	110 Deg Blum Hinge

Hinges Plates


6	Std Inline Hinge Plate


Miscellaneous


1	Oval Hanging Rail	Hanging Rail - Oval - White	Cut to 772mm


Hardware

6	Hinge	110 Deg Blum Hinge	47
6	Hinge Plate	Std Inline Hinge Plate	19.5(

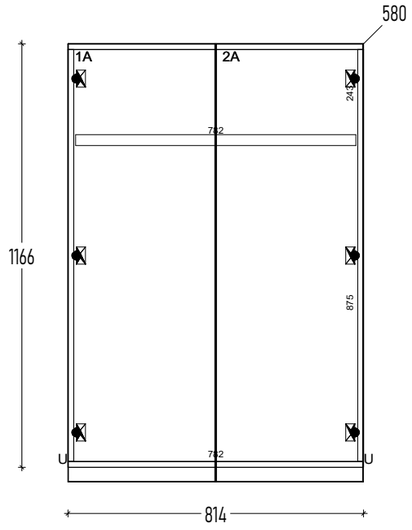

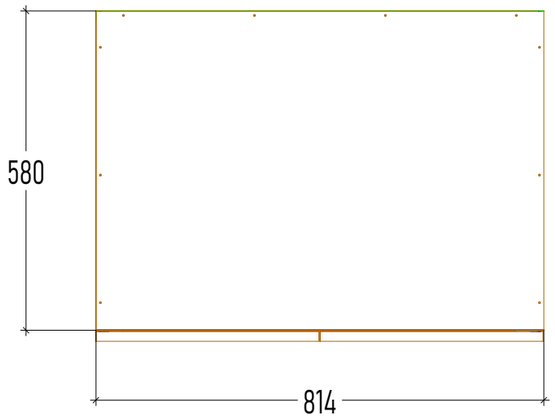

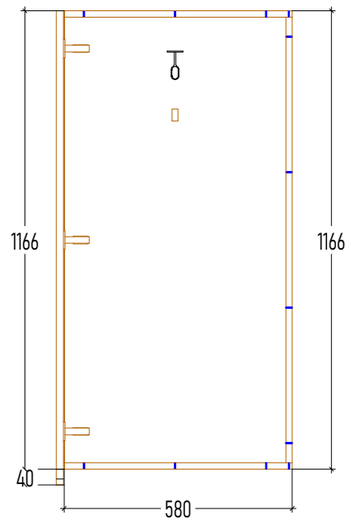

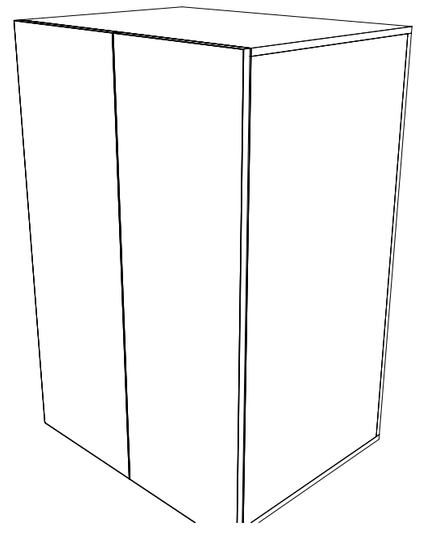

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 1

Bot Reveal = -40

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 1 Robe) - Wall #4

Date: 28/09/26

Assembly #27 - STD WALL 2 DOOR
814 x 810 x 580 (1)

Doors

2	405	810	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	778	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	778	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	814	778	Unfinished Back	16mm HMR White	
1	580	814	Top	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	580	814	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	554	780	Adjustable Shelf	16mm HMR White	

Hinges


4 110 Deg Blum Hinge


Hinges Plates


4 Std Inline Hinge Plate


Hardware

4	Hinge	110 Deg Blum Hinge	47
4	Hinge Plate	Std Inline Hinge Plate	19.5(

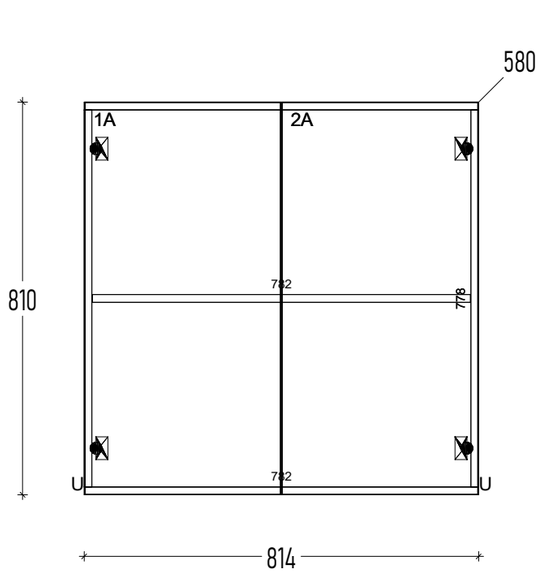

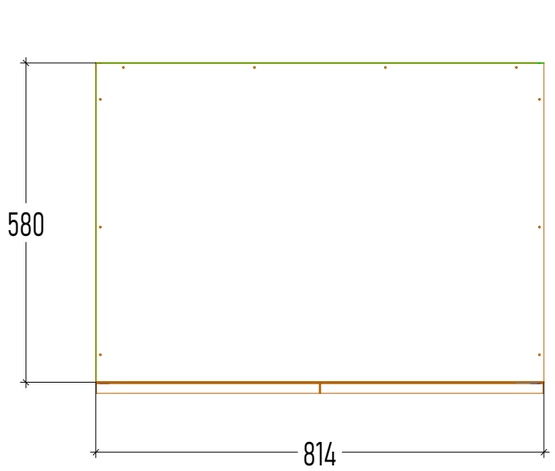

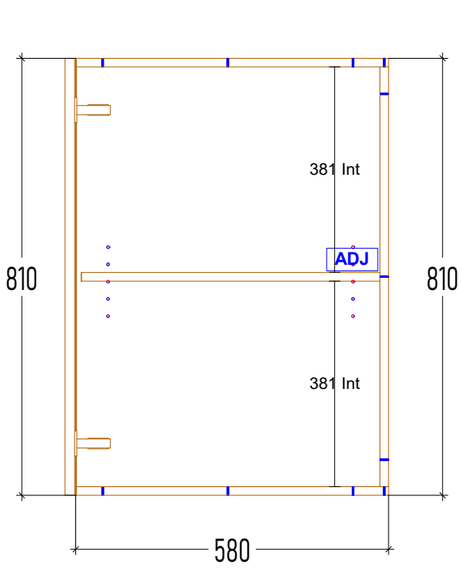

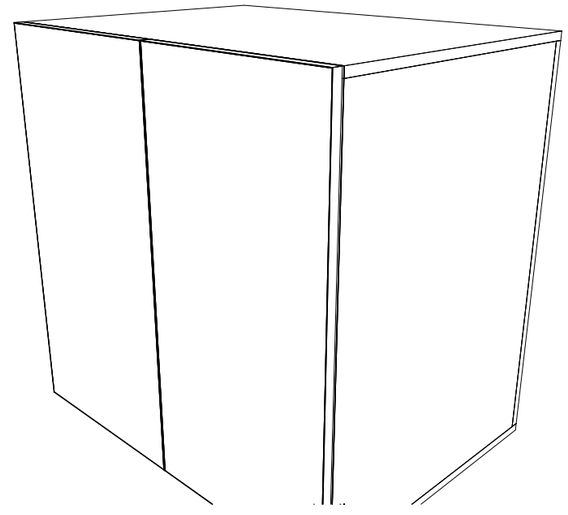

Top Reveal = 0

LHS Reveal = 1 RHS Reveal = 1

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 1 Robe) - Wall #4

Date: 28/09/26

Assembly #28 - STD WALL 2 DOOR
814 x 1166 x 580 (1)

Doors

2	405	1206	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	1134	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	1134	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	814	1134	Unfinished Back	16mm HMR White	
1	580	814	Top	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	580	814	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU

Hinges

6	110 Deg Blum Hinge

Hinges Plates


6	Std Inline Hinge Plate


Miscellaneous


1	Oval Hanging Rail	Hanging Rail - Oval - White	Cut to 772mm


Hardware

6	Hinge	110 Deg Blum Hinge	47
6	Hinge Plate	Std Inline Hinge Plate	19.5(

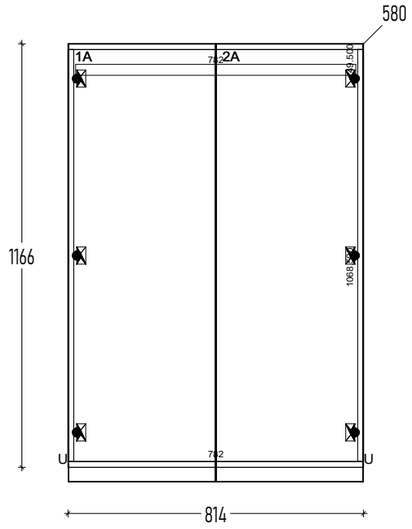

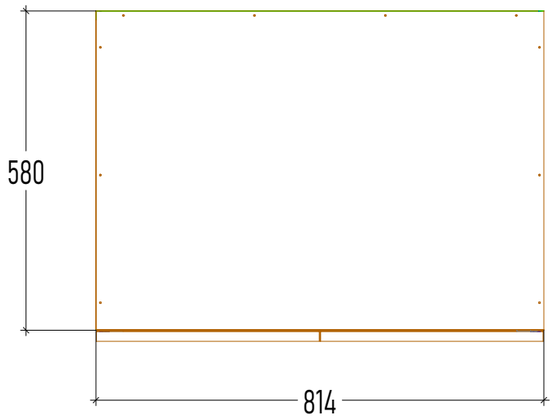

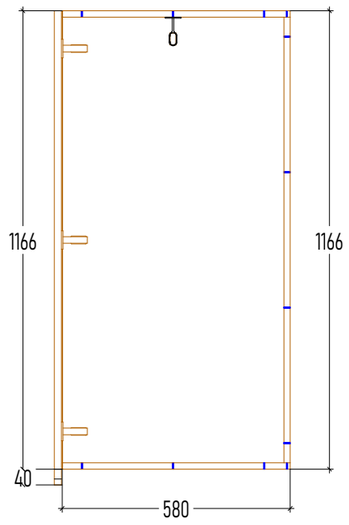

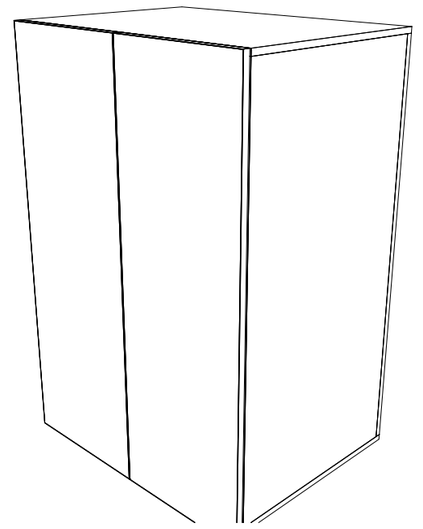

Top Reveal = 0

LHS Reveal = 1 RHS Reveal = 1

Bot Reveal = -40

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 1 Robe) - Wall #4

Date: 28/09/26

Assembly #29 - STD WALL 2 DOOR
814 x 810 x 580 (1)

Doors

2	405.500	810	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	778	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	778	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	814	778	Unfinished Back	16mm HMR White	
1	580	814	Top	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	580	814	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	554	780	Adjustable Shelf	16mm HMR White	

Hinges


4 110 Deg Blum Hinge


Hinges Plates


4 Std Inline Hinge Plate


Hardware

4	Hinge	110 Deg Blum Hinge	47
4	Hinge Plate	Std Inline Hinge Plate	19.5(

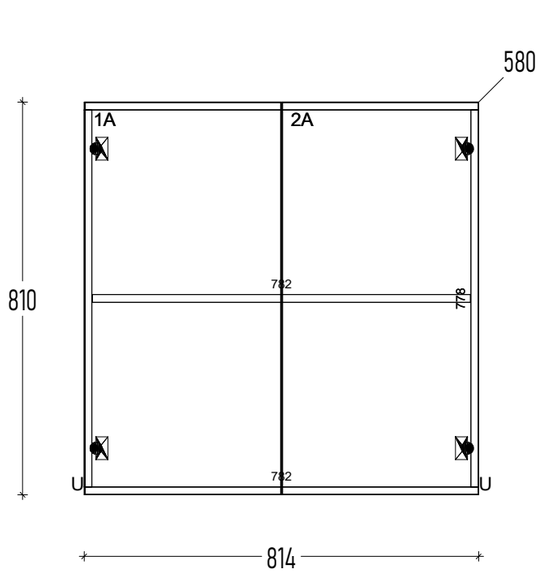

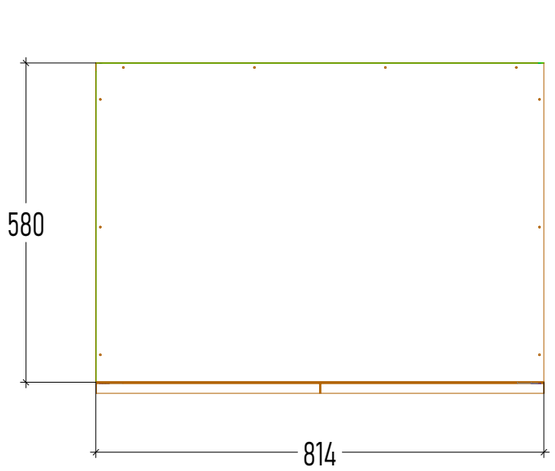

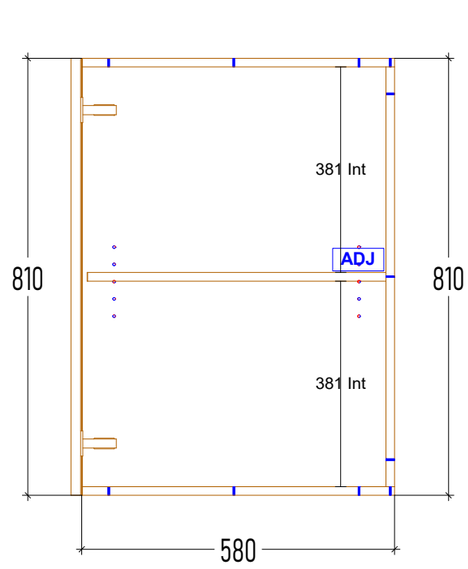

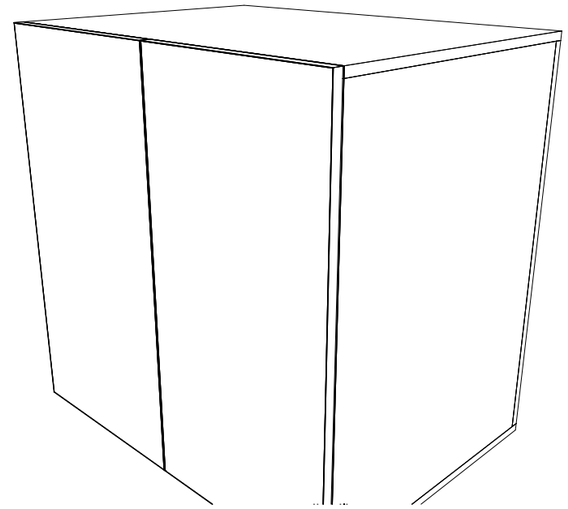

Top Reveal = 0

LHS Reveal = 1 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 1 Robe) - Wall #4


Date: 28/09/26


Assembly #41 - Toe Assembly
2502 x 100 x 580 (1)


Parts Within Cabinet

6	80	497	Sleeper	16mm Packing Sheet
6	80	497	Top Sleeper	16mm Packing Sheet
1	100	2502	Front Toe	16mm Packing Sheet
1	2502	120	Front Kick Face	18mm Polytec Florentine Walnut Woodma.
1	100	2502	Back Toe	16mm Packing Sheet









Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen


Bed 4 Robe) - Wall #4


Date: 28/09/26

Assembly #42 - Tall Panel to Floor
18 x 2960 x 600 (1)

Parts Within Cabinet

1	620	2980	Panel	18mm Polytec Florentine Walnut Woodma





Top Reveal = 0

LHS Reveal = 2 RHS Reveal = 0

Bot Reveal = 0

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Hor Reveal = 0

Vert Reveal = 2

Bed 4 Robe) - Wall #4

Date: 28/09/26

Assembly #43 - C BASE 4 DRAWER
814 x 884 x 580 (1)

Drawer Fronts

1	811	183	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	
3	811	210	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	852	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	852	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	814	852	Unfinished Back	16mm HMR White	
1	542	814	Top	16mm HMR White	
1	580	814	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	747	540	Drawer Box Bottom 1	16mm HMR White	
1	101	744	Drawer Box Back 1	16mm HMR White	
1	747	540	Drawer Box Bottom 2	16mm HMR White	
1	148	744	Drawer Box Back 2	16mm HMR White	
1	747	540	Drawer Box Bottom 3	16mm HMR White	
1	148	744	Drawer Box Back 3	16mm HMR White	
1	747	540	Drawer Box Bottom 4	16mm HMR White	
1	148	744	Drawer Box Back 4	16mm HMR White	

Drawers

1	P	LBox Wte Bmn 70 Kx550
3	P	LBox Wte Bmn 70 Cx550

Handles


4	240 overall - 192mm C - Brave - Metallic Brown


Miscellaneous


8	Legrabox Bmn 70kg	LBox DG Bmn 70Kg 550
2	Legrabox Drw Side	LBox Side Wte K 550
2	Legrabox Front Brkt	LBox Fnt Brkt K Exp
2	Legrabox Back Brkt	LBox Back Brkt Wte K
6	Legrabox Drw Side	LBox Side Wte C 550
12	Legrabox Front Brkt	LBox Fnt Brkt M Exp
6	Legrabox Back Brkt	LBox Back Brkt Wte C

Hardware

4	Drawer Pull	240 overall - 192mm C - Brave	240
4	Drawer Box Base Bracket	Blum Drawer Base Support	20
1 P	Drawer Guide	LBox Wte Bmn 70 Kx550	550
3 P	Drawer Guide	LBox Wte Bmn 70 Cx550	550

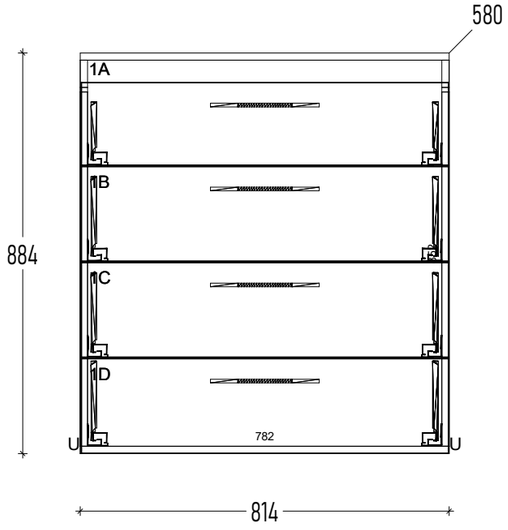

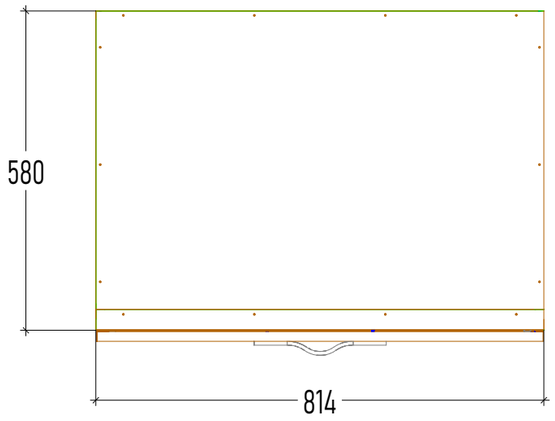

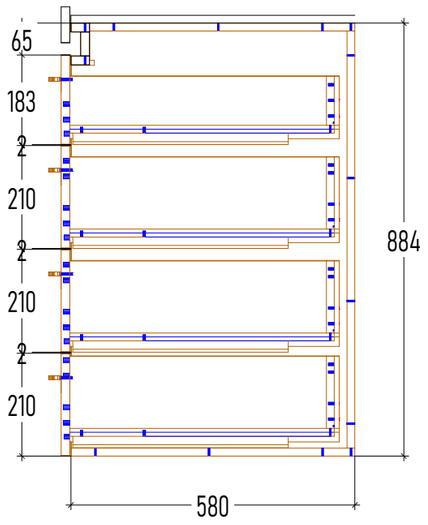



Top Reveal = 65

LHS Reveal = 2 RHS Reveal = 1

Bot Reveal = 0

Hor Reveal = 2

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen


Bed 4 Robe) - Wall #4


Date: 28/09/26


Assembly #43.1 - C WALL OPEN
814 x 85 x 38 (1)


Parts Within Cabinet

1	814	49	C Shape Fingerpull Rail	18mm Polytec Florentine Walnut Woodma*** MAKE INTO C SHAPE FINGERF
1	38	814	C Shape Fingerpull Top	18mm Polytec Florentine Walnut Woodma*** MAKE INTO C SHAPE FINGERF
1	38	814	C Shape Fingerpull Bottom	18mm Polytec Florentine Walnut Woodma*** MAKE INTO C SHAPE FINGERF





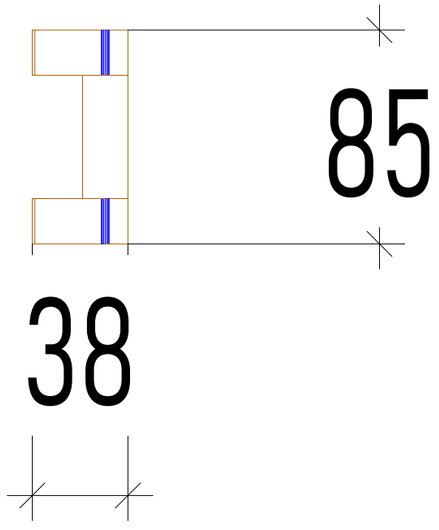

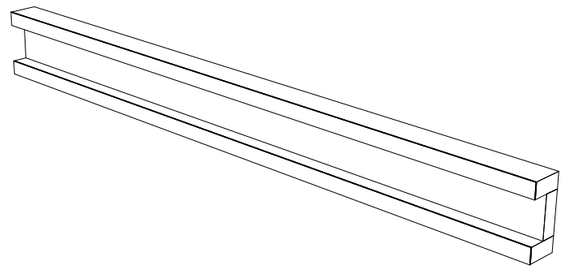

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 4 Robe) - Wall #4

Date: 28/09/26

Assembly #44 - C BASE 4 DRAWER
814 x 884 x 580 (1)

Drawer Fronts

1	812	183	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	
3	812	210	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	852	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	852	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	814	852	Unfinished Back	16mm HMR White	
1	542	814	Top	16mm HMR White	
1	580	814	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	747	540	Drawer Box Bottom 1	16mm HMR White	
1	101	744	Drawer Box Back 1	16mm HMR White	
1	747	540	Drawer Box Bottom 2	16mm HMR White	
1	148	744	Drawer Box Back 2	16mm HMR White	
1	747	540	Drawer Box Bottom 3	16mm HMR White	
1	148	744	Drawer Box Back 3	16mm HMR White	
1	747	540	Drawer Box Bottom 4	16mm HMR White	
1	148	744	Drawer Box Back 4	16mm HMR White	

Drawers

1	P	LBox Wte Bmn 70 Kx550
3	P	LBox Wte Bmn 70 Cx550

Handles


4	240 overall - 192mm C - Brave - Metallic Brown


Miscellaneous


8	Legrabox Bmn 70kg	LBox DG Bmn 70Kg 550
2	Legrabox Drw Side	LBox Side Wte K 550
2	Legrabox Front Brkt	LBox Fnt Brkt K Exp
2	Legrabox Back Brkt	LBox Back Brkt Wte K
6	Legrabox Drw Side	LBox Side Wte C 550
12	Legrabox Front Brkt	LBox Fnt Brkt M Exp
6	Legrabox Back Brkt	LBox Back Brkt Wte C

Hardware

4	Drawer Pull	240 overall - 192mm C - Brave	240
4	Drawer Box Base Bracket	Blum Drawer Base Support	20
1 P	Drawer Guide	LBox Wte Bmn 70 Kx550	550
3 P	Drawer Guide	LBox Wte Bmn 70 Cx550	550

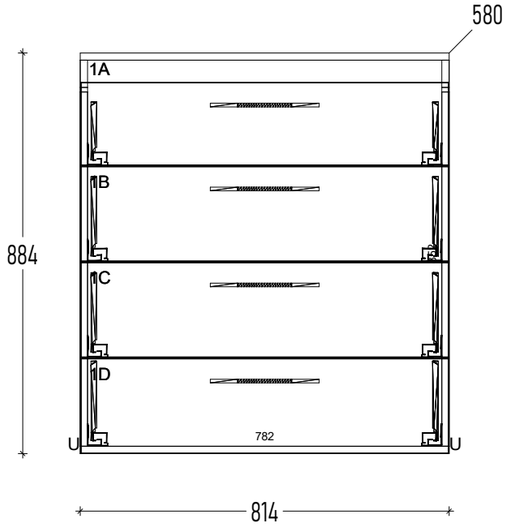

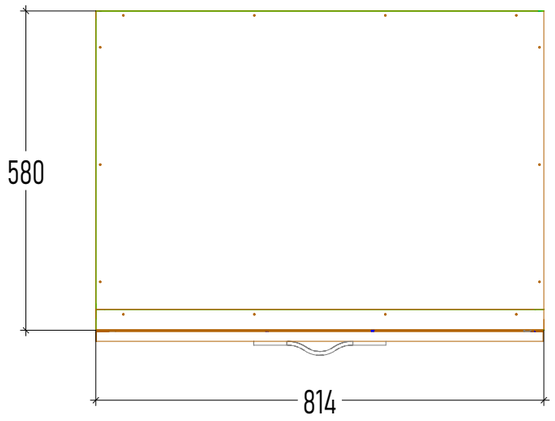

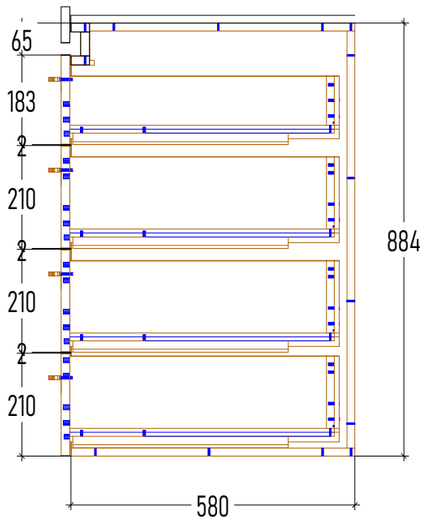



Top Reveal = 65

LHS Reveal = 1 RHS Reveal = 1

Bot Reveal = 0

Hor Reveal = 2

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen


Bed 4 Robe) - Wall #4


Date: 28/09/26


Assembly #44.1 - C WALL OPEN
814 x 85 x 38 (1)


Parts Within Cabinet

1	814	49	C Shape Fingerpull Rail	18mm Polytec Florentine Walnut Woodma*** MAKE INTO C SHAPE FINGERF
1	38	814	C Shape Fingerpull Top	18mm Polytec Florentine Walnut Woodma*** MAKE INTO C SHAPE FINGERF
1	38	814	C Shape Fingerpull Bottom	18mm Polytec Florentine Walnut Woodma*** MAKE INTO C SHAPE FINGERF





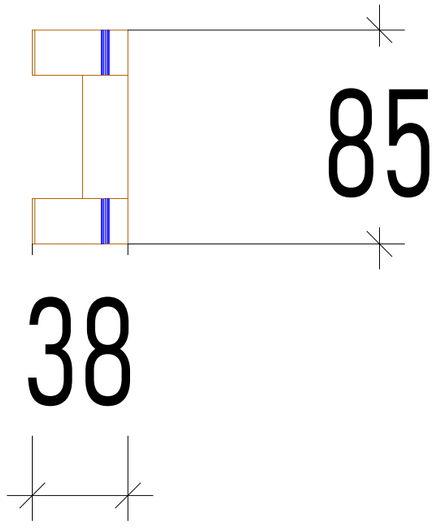

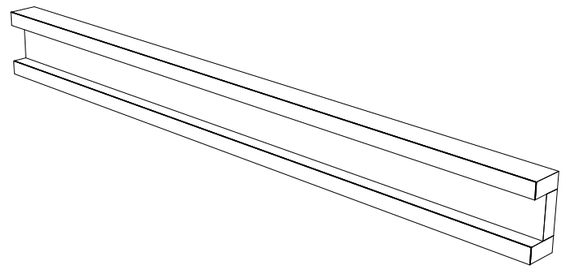

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 4 Robe) - Wall #4

Date: 28/09/26

Assembly #45 - Std Tall 1 Door
407 x 2050 x 580 (1)

Doors

1	406	2050	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	2018	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	2018	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	407	2018	Unfinished Back	16mm HMR White	
1	580	407	Top	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	580	407	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU

Handles

1	1040 OFFSET - 992mm C - Brave - Metallic Brown

Hinges

4	110 Deg Blum Hinge

Hinges Plates


4	Std Inline Hinge Plate


Miscellaneous


2	Rectangle Hanging Rail	Hanging Rail - Rectangular - Black	Cut to 365mm


Hardware

1	Door Pull	1040 OFFSET - 992mm C - Bra	1040
4	Hinge	110 Deg Blum Hinge	47
4	Hinge Plate	Std Inline Hinge Plate	19.5(



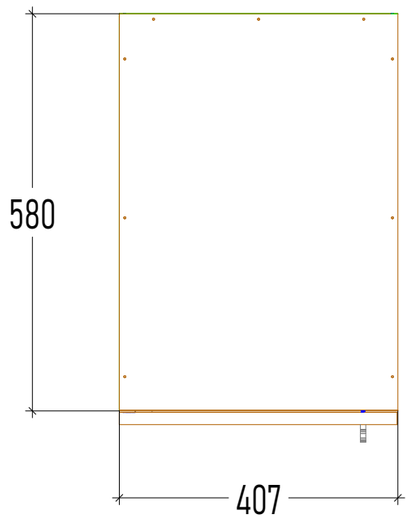





Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 1

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 4 Robe) - Wall #4

Date: 28/09/26

Assembly #46 - Std Tall 1 Door
407 x 2050 x 580 (1)

Doors

1	406	2050	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	2018	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	2018	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	407	2018	Unfinished Back	16mm HMR White	
1	580	407	Top	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	580	407	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU
2	554	373	Adjustable Shelf	16mm HMR White	

Handles

1	1040 OFFSET - 992mm C - Brave - Metallic Brown	

Hinges

4	110 Deg Blum Hinge	

Hinges Plates


4	Std Inline Hinge Plate	


Miscellaneous


1	Rectangle Hanging Rail	Hanging Rail - Rectangular - Black	Cut to 365mm


Hardware

1	Door Pull	1040 OFFSET - 992mm C - Bra	1040
4	Hinge	110 Deg Blum Hinge	47
4	Hinge Plate	Std Inline Hinge Plate	19.5(



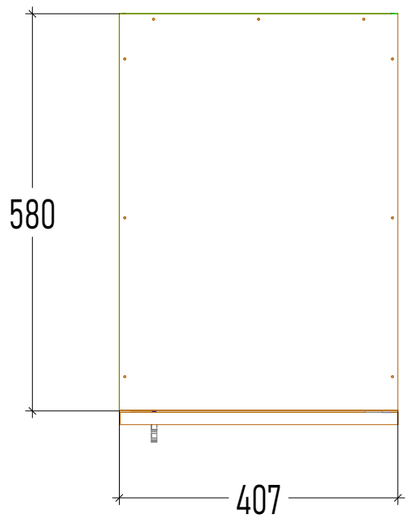





Top Reveal = 0

LHS Reveal = 1 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen


Bed 4 Robe) - Wall #4


Date: 28/09/26


Assembly #47 - Tall Face Filler
60 x 2860 x 580 (1)

Parts Within Cabinet

1	60	2860	Filler	18mm Polytec Florentine Walnut Woodma









Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen


Bed 4 Robe) - Wall #4


Date: 28/09/26


Assembly #48 - BULKHEAD WALL OPEN
2502 x 40 x 580 (1)


Parts Within Cabinet

1	568	2440	Bulkhead Bottom	12mm Board	
1	580	40	Bulkhead Left End	12mm Board	45* 1 SHORT
1	2502	40	Bulkhead Face Panel	12mm Board	45* 1 SHORT







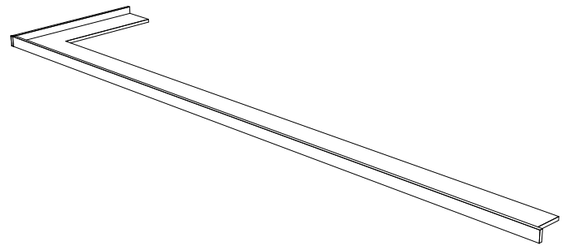

Top Reveal = 0

LHS Reveal = 2 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 0

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 4 Robe) - Wall #4

Date: 28/09/26

Assembly #49 - STD WALL 2 DOOR
814 x 810 x 580 (1)

Doors

2	405.500	810	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	778	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	778	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	814	778	Unfinished Back	16mm HMR White	
1	580	814	Top	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	580	814	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	554	780	Adjustable Shelf	16mm HMR White	

Hinges


4 110 Deg Blum Hinge


Hinges Plates


4 Std Inline Hinge Plate


Hardware

4	Hinge	110 Deg Blum Hinge	47
4	Hinge Plate	Std Inline Hinge Plate	19.5(

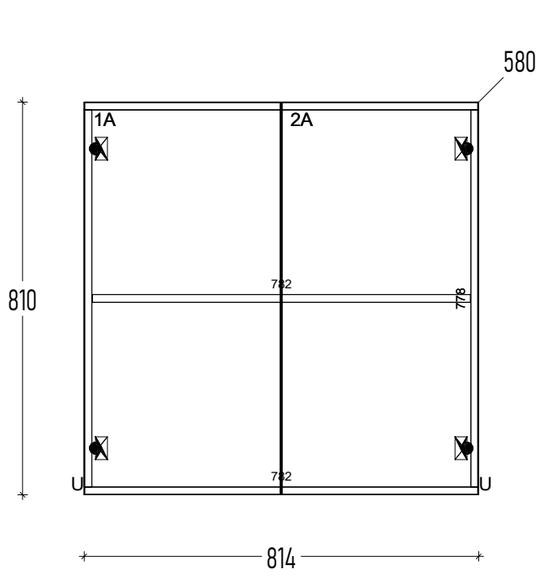

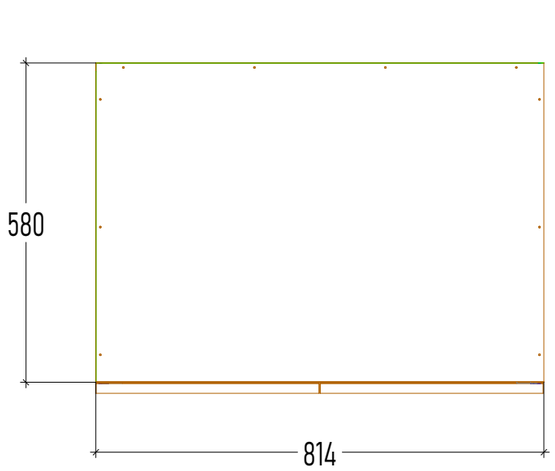

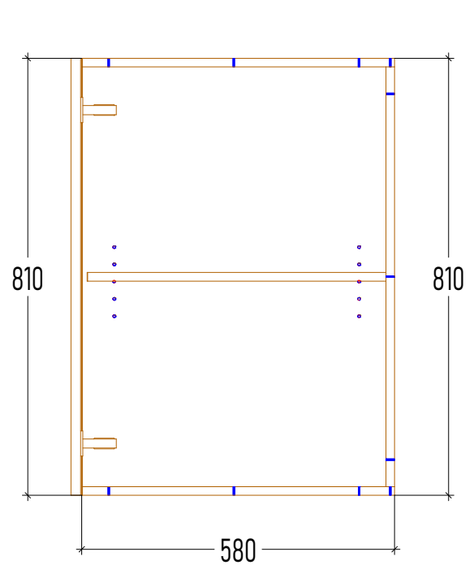

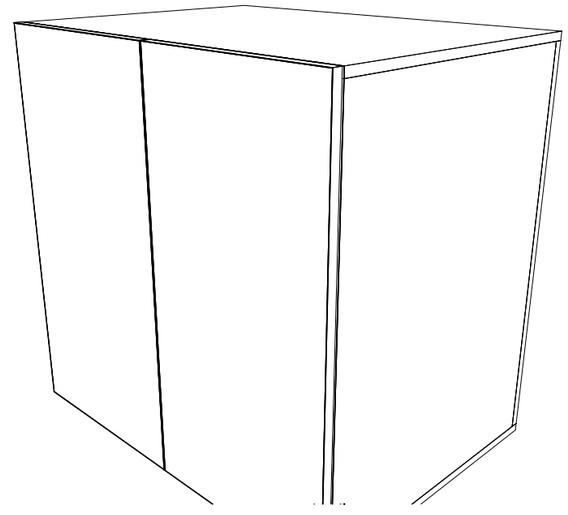

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 1

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 4 Robe) - Wall #4

Date: 28/09/26

Assembly #50 - STD WALL 2 DOOR
814 x 1166 x 580 (1)

Doors

2	405.500	1206	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	1134	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	1134	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	814	1134	Unfinished Back	16mm HMR White	
1	580	814	Top	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	580	814	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU

Hinges

6	110 Deg Blum Hinge

Hinges Plates


6	Std Inline Hinge Plate


Miscellaneous


1	Oval Hanging Rail	Hanging Rail - Oval - White	Cut to 772mm


Hardware

6	Hinge	110 Deg Blum Hinge	47
6	Hinge Plate	Std Inline Hinge Plate	19.5(

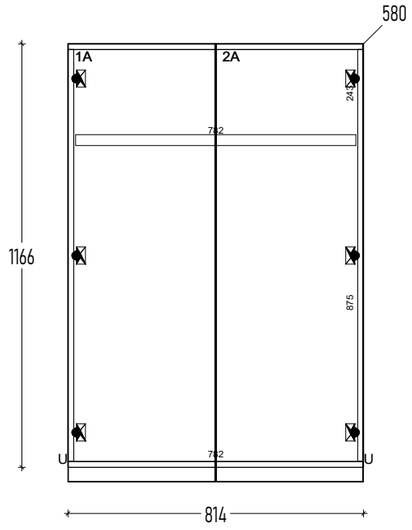

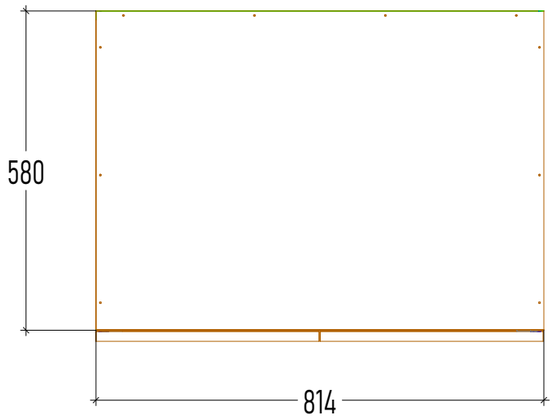

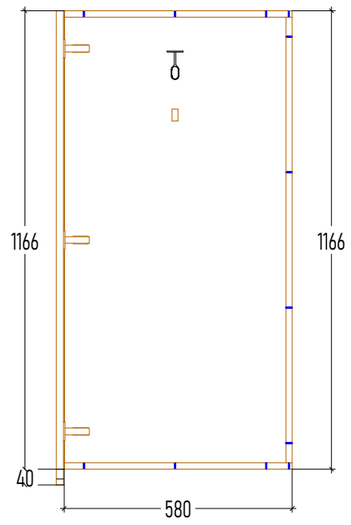

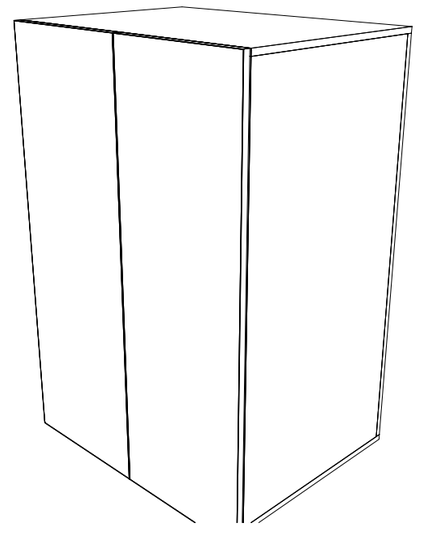

Top Reveal = 0

LHS Reveal = 0 RHS Reveal = 1

Bot Reveal = -40

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 4 Robe) - Wall #4

Date: 28/09/26

Assembly #51 - STD WALL 2 DOOR
814 x 810 x 580 (1)

Doors

2	405	810	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	778	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	778	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	814	778	Unfinished Back	16mm HMR White	
1	580	814	Top	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	580	814	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	554	780	Adjustable Shelf	16mm HMR White	

Hinges


4 110 Deg Blum Hinge


Hinges Plates


4 Std Inline Hinge Plate


Hardware

4	Hinge	110 Deg Blum Hinge	47
4	Hinge Plate	Std Inline Hinge Plate	19.5(

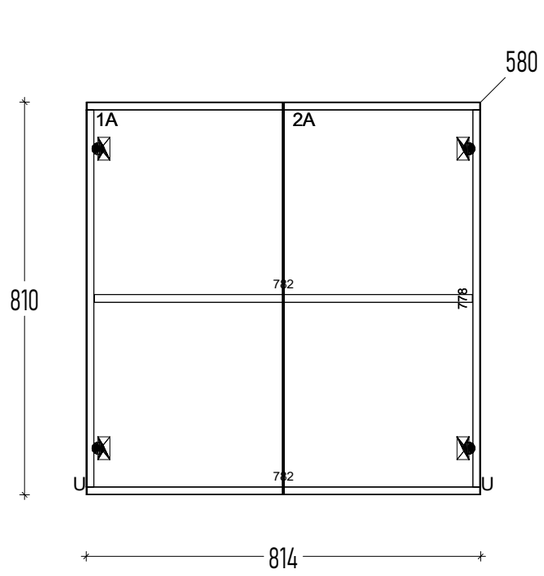

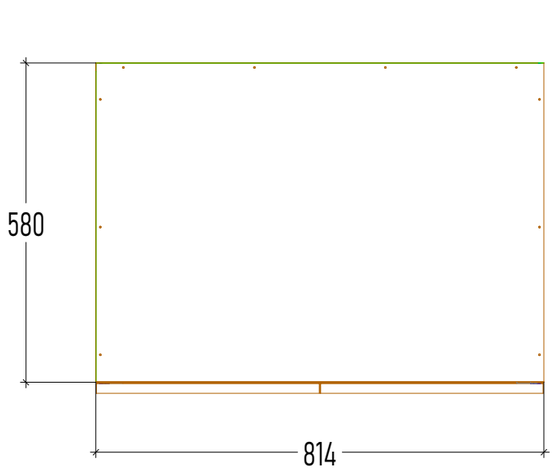

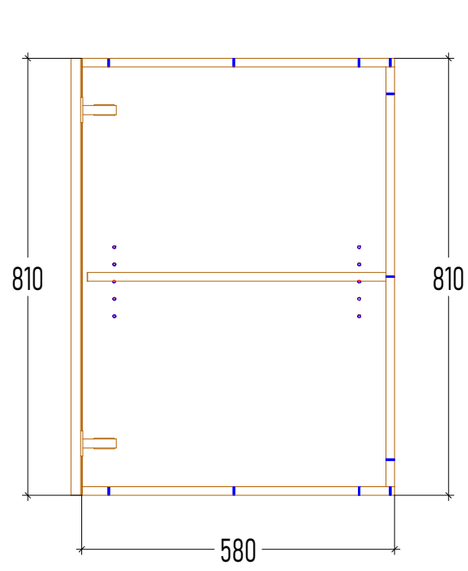

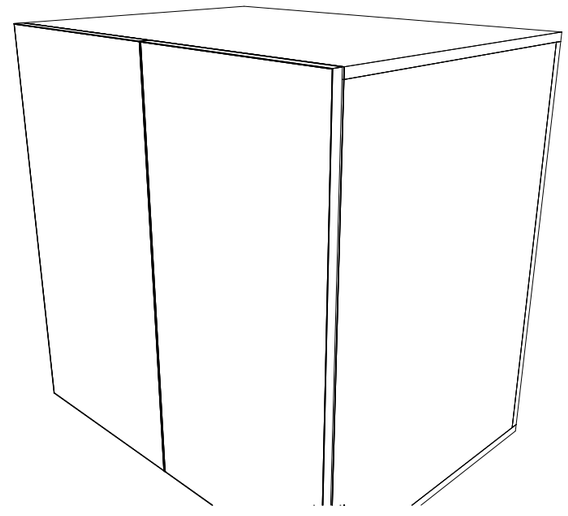

Top Reveal = 0

LHS Reveal = 1 RHS Reveal = 1

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 4 Robe) - Wall #4

Date: 28/09/26

Assembly #52 - STD WALL 2 DOOR
814 x 1166 x 580 (1)

Doors

2	405	1206	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	1134	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	1134	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	814	1134	Unfinished Back	16mm HMR White	
1	580	814	Top	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	580	814	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU

Hinges

6	110 Deg Blum Hinge

Hinges Plates


6	Std Inline Hinge Plate


Miscellaneous


1	Oval Hanging Rail	Hanging Rail - Oval - White	Cut to 772mm


Hardware

6	Hinge	110 Deg Blum Hinge	47
6	Hinge Plate	Std Inline Hinge Plate	19.5(

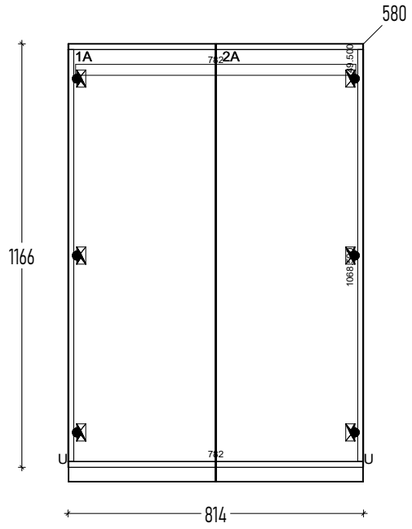

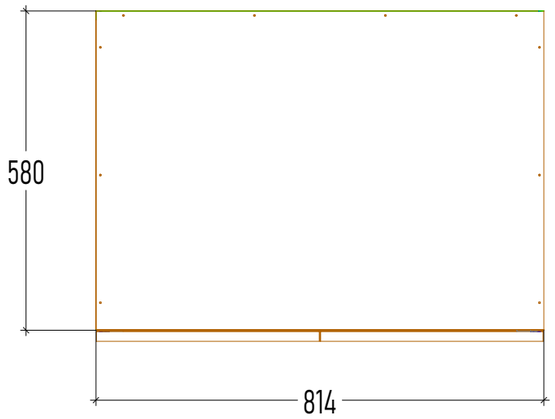

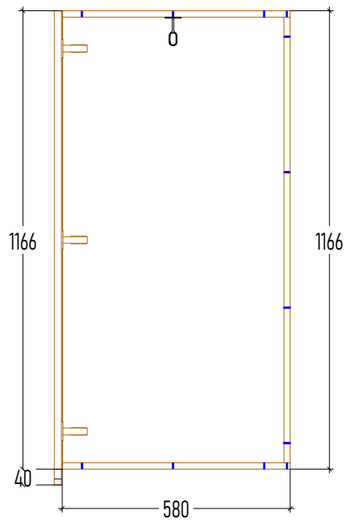

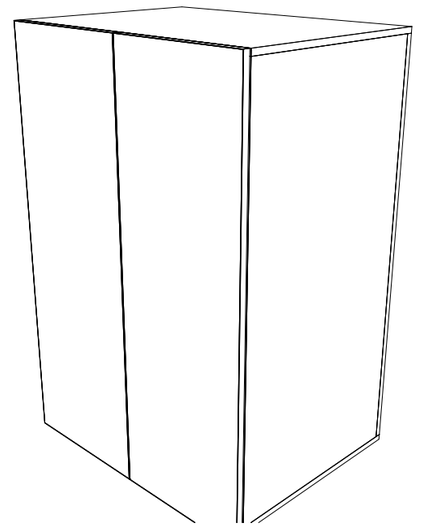

Top Reveal = 0

LHS Reveal = 1 RHS Reveal = 1

Bot Reveal = -40

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 4 Robe) - Wall #4

Date: 28/09/26

Assembly #53 - STD WALL 2 DOOR
814 x 810 x 580 (1)

Doors

2	405.500	810	Vertical Grain	18mm Polytec Florentine Walnut Woodmatt	

Parts Within Cabinet

1	564	778	Left End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	564	778	Right End	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	814	778	Unfinished Back	16mm HMR White	
1	580	814	Top	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	580	814	Bottom	16mm HMR White	*** EDGE IN FLORENTINE WALNU
1	554	780	Adjustable Shelf	16mm HMR White	

Hinges


4 110 Deg Blum Hinge


Hinges Plates


4 Std Inline Hinge Plate


Hardware

4	Hinge	110 Deg Blum Hinge	47
4	Hinge Plate	Std Inline Hinge Plate	19.5(

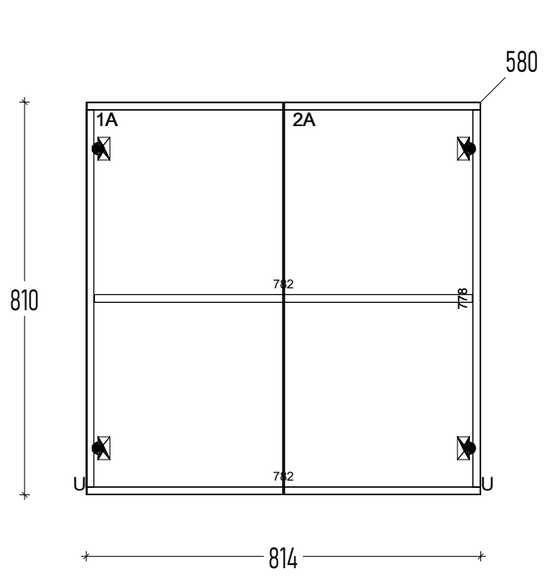

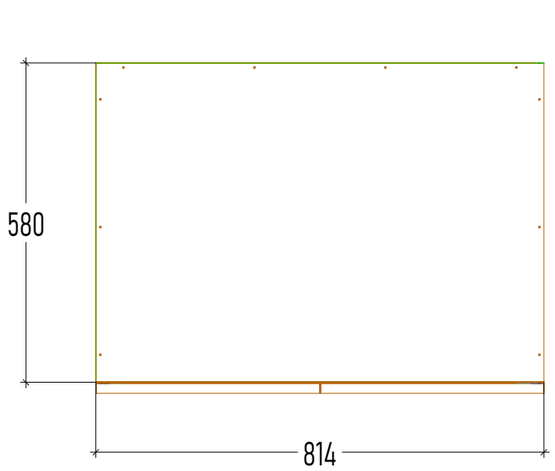

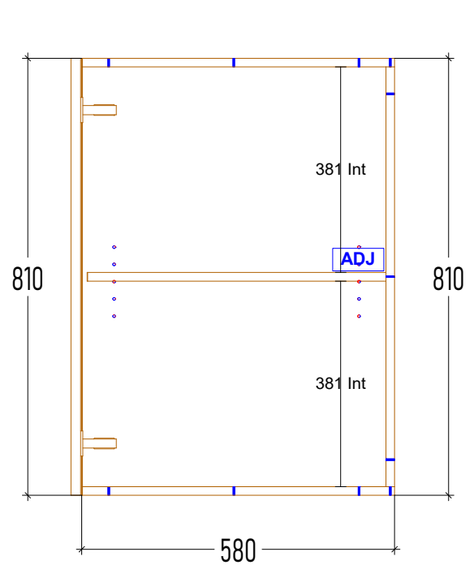

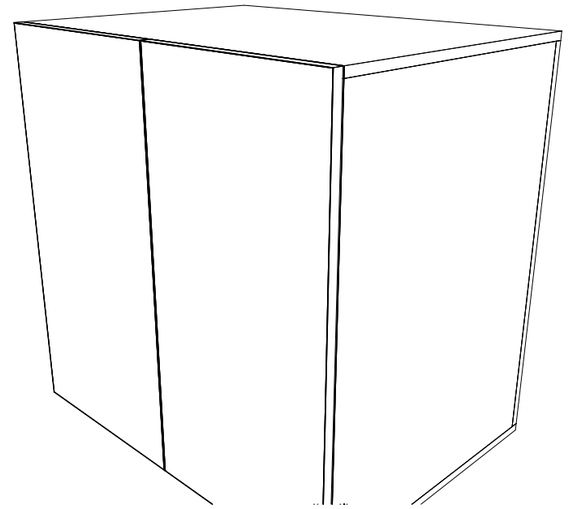

Top Reveal = 0

LHS Reveal = 1 RHS Reveal = 0

Bot Reveal = 0

Hor Reveal = 0

Vert Reveal = 2

J1093 - 62 Florizel Street - Hallway Laundry-Linen

Bed 4 Robe) - Wall #4

Date: 28/09/26
