

Panel Stock

1	80	379.4	Sleeper	16mm Packing Sheet
6	80	379.4	Spreader	16mm Packing Sheet
5	80	379.4	Sleeper	16mm Packing Sheet
1	100	2434	Front Toe	16mm Packing Sheet
1	100	2434	Back Toe	16mm Packing Sheet
1	120	2477	Skin - Front Toe	18mm Laminex Terril Flint

Assembly #1 - Toe Assembly

2434 x 100 x 430 (1)



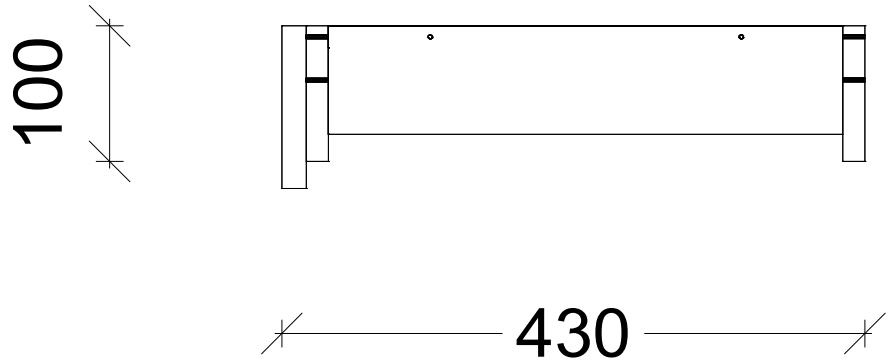

Assembly #1 - Toe Assembly

** FTAB

LHS Reveal = 2 | RHS Reveal = 2 | Hor Reveal = 2

Top Reveal = 3 | Bot Reveal = 0

Toe Height = 100 | Toe Recess = 18

Left End = Unfinished | Right End = Unfinished | Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #3

Date: 22/10/26

Drawer Fronts

2	600.5	397.5	Horizontal Grain	18mm Laminex Aged Walnut M

Panel Stock

1	464	768	Left End	16mm Carcase White Texture
1	464	768	Right End	16mm Carcase White Texture
1	603.5	768	Unfinished Back	16mm Carcase White Texture
1	480	603.5	Top	16mm Carcase White Texture
1	480	603.5	Bottom	16mm Carcase White Texture
1	536.5	440	Drawer Box Bottom 1	16mm Carcase White Texture
1	280	533.5	Drawer Box Back 1	16mm Carcase White Texture
1	536.5	440	Drawer Box Bottom 2	16mm Carcase White Texture
1	280	533.5	Drawer Box Back 2	16mm Carcase White Texture

Hardware


2	Drawer Pull	200mm Ferrara Black 160mm Centre	200
2 P	Drawer Guide	LBox Wte Bmn 40 Fx450	450


Miscellaneous

4	Legrabox Bmn 40kg	370	LBox DG Bmn 40Kg 450
4	Legrabox Drw Side	450	LBox Side Wte F 450
12	Legrabox Front Brkt	59.5	LBox Fnt Brkt M Exp
4	Legrabox Back Brkt	226.4	LBox Back Brkt Wte F

Assembly #2 - 2 Drawer Bank

603.5 x 800 x 480 (1)

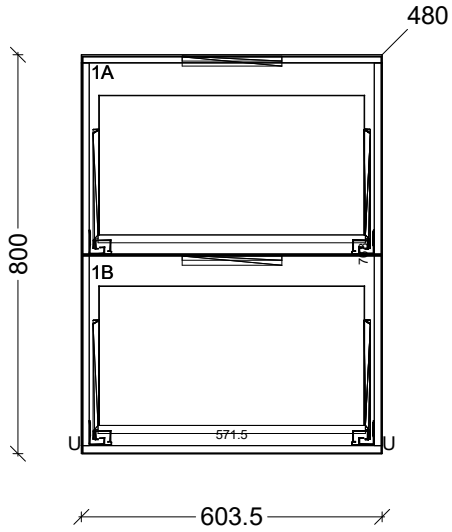

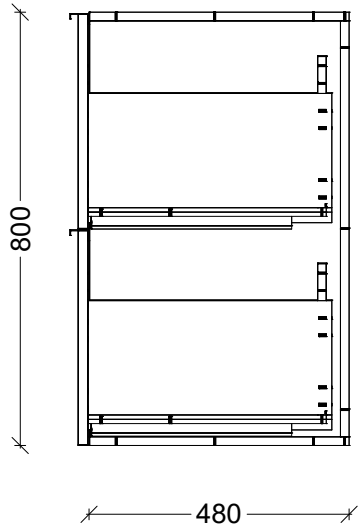

Assembly #2 - 2 Drawer Bank

** FTAB

LHS Reveal = 2 | RHS Reveal = 1 | Hor Reveal = 2

Top Reveal = 3 | Bot Reveal = 0

Toe Height = 0 | Toe Recess = 50

Left End = Unfinished | Right End = Unfinished | Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #3

Date: 22/10/26

Drawer Fronts

2	601.5	397.5	Horizontal Grain	18mm Laminex Aged Walnut M

Panel Stock

1	464	768	Left End	16mm Carcase White Texture
1	464	768	Right End	16mm Carcase White Texture
1	603.5	768	Unfinished Back	16mm Carcase White Texture
1	480	603.5	Top	16mm Carcase White Texture
1	480	603.5	Bottom	16mm Carcase White Texture
1	536.5	440	Drawer Box Bottom 1	16mm Carcase White Texture
1	280	533.5	Drawer Box Back 1	16mm Carcase White Texture
1	536.5	440	Drawer Box Bottom 2	16mm Carcase White Texture
1	280	533.5	Drawer Box Back 2	16mm Carcase White Texture

Hardware


2	Drawer Pull	200mm Ferrara Black 160mm Centre	200
2 P	Drawer Guide	LBox Wte Bmn 40 Fx450	450


Miscellaneous

4	Legrabox Bmn 40kg	370	LBox DG Bmn 40Kg 450
4	Legrabox Drw Side	450	LBox Side Wte F 450
12	Legrabox Front Brkt	59.5	LBox Fnt Brkt M Exp
4	Legrabox Back Brkt	226.4	LBox Back Brkt Wte F

Assembly #3 - 2 Drawer Bank

603.5 x 800 x 480 (1)

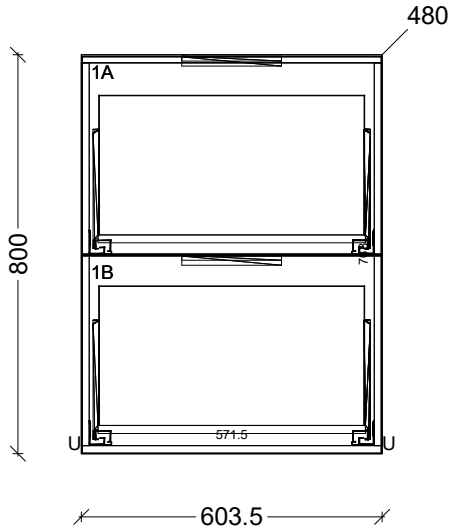

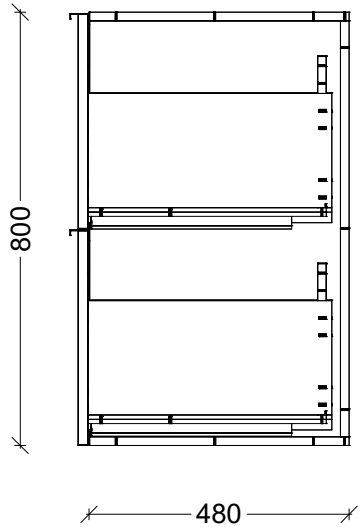

Assembly #3 - 2 Drawer Bank

** FTAB

LHS Reveal = 1 | RHS Reveal = 1 | Hor Reveal = 2

Top Reveal = 3 | Bot Reveal = 0

Toe Height = 0 | Toe Recess = 50

Left End = Unfinished | Right End = Unfinished | Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #3

Date: 22/10/26

Drawer Fronts

2	601.5	397.5	Horizontal Grain	18mm Laminex Aged Walnut M

Panel Stock

1	464	768	Left End	16mm Carcase White Texture
1	464	768	Right End	16mm Carcase White Texture
1	603.5	768	Unfinished Back	16mm Carcase White Texture
1	480	603.5	Top	16mm Carcase White Texture
1	480	603.5	Bottom	16mm Carcase White Texture
1	536.5	440	Drawer Box Bottom 1	16mm Carcase White Texture
1	280	533.5	Drawer Box Back 1	16mm Carcase White Texture
1	536.5	440	Drawer Box Bottom 2	16mm Carcase White Texture
1	280	533.5	Drawer Box Back 2	16mm Carcase White Texture

Hardware


2	Drawer Pull	200mm Ferrara Black 160mm Centre	200
2 P	Drawer Guide	LBox Wte Bmn 40 Fx450	450


Miscellaneous

4	Legrabox Bmn 40kg	370	LBox DG Bmn 40Kg 450
4	Legrabox Drw Side	450	LBox Side Wte F 450
12	Legrabox Front Brkt	59.5	LBox Fnt Brkt M Exp
4	Legrabox Back Brkt	226.4	LBox Back Brkt Wte F

Assembly #4 - 2 Drawer Bank

603.5 x 800 x 480 (1)

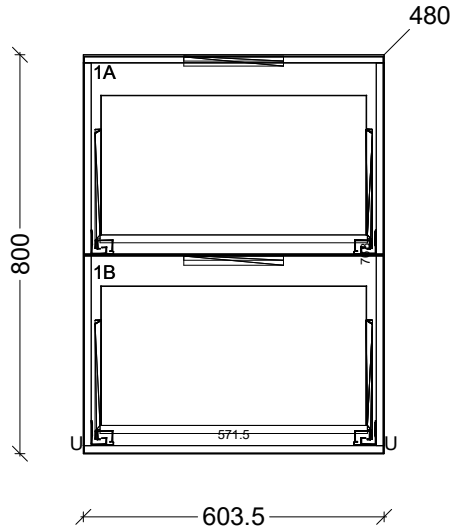

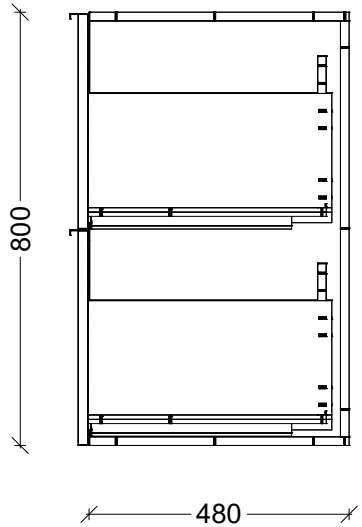

Assembly #4 - 2 Drawer Bank

** FTAB

LHS Reveal = 1 | RHS Reveal = 1 | Hor Reveal = 2

Top Reveal = 3 | Bot Reveal = 0

Toe Height = 0 | Toe Recess = 50

Left End = Unfinished | Right End = Unfinished | Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #3

Date: 22/10/26

Drawer Fronts

2	600.5	397.5	Horizontal Grain	18mm Laminex Aged Walnut M

Panel Stock

1	464	768	Left End	16mm Carcase White Texture
1	464	768	Right End	16mm Carcase White Texture
1	603.5	768	Unfinished Back	16mm Carcase White Texture
1	480	603.5	Top	16mm Carcase White Texture
1	480	603.5	Bottom	16mm Carcase White Texture
1	536.5	440	Drawer Box Bottom 1	16mm Carcase White Texture
1	280	533.5	Drawer Box Back 1	16mm Carcase White Texture
1	536.5	440	Drawer Box Bottom 2	16mm Carcase White Texture
1	280	533.5	Drawer Box Back 2	16mm Carcase White Texture

Hardware


2	Drawer Pull	200mm Ferrara Black 160mm Centre	200
2 P	Drawer Guide	LBox Wte Bmn 40 Fx450	450


Miscellaneous

4	Legrabox Bmn 40kg	370	LBox DG Bmn 40Kg 450
4	Legrabox Drw Side	450	LBox Side Wte F 450
12	Legrabox Front Brkt	59.5	LBox Fnt Brkt M Exp
4	Legrabox Back Brkt	226.4	LBox Back Brkt Wte F

Assembly #5 - 2 Drawer Bank

603.5 x 800 x 480 (1)

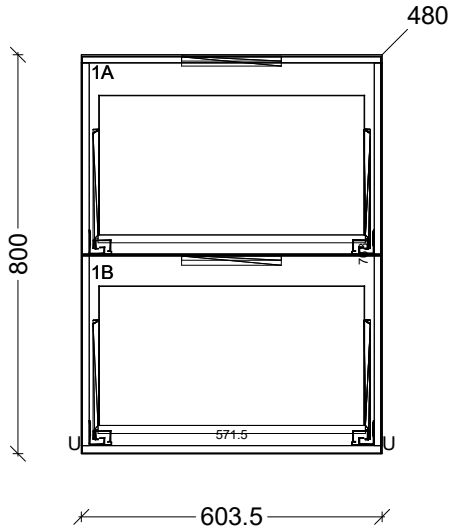

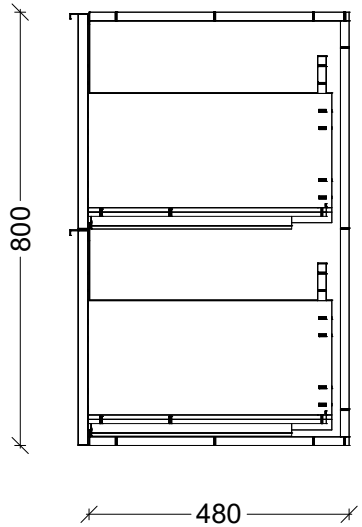

Assembly #5 - 2 Drawer Bank

** FTAB

LHS Reveal = 1 | RHS Reveal = 2 | Hor Reveal = 2

Top Reveal = 3 | Bot Reveal = 0

Toe Height = 0 | Toe Recess = 50

Left End = Unfinished | Right End = Unfinished | Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #3


Date: 22/10/26


Panel Stock

1	120	2100	Filler	18mm Laminex Terril Flint

Assembly #6 - Flush Face Filler - Rip Return

20 x 2100 x 480 (1)





Assembly #6 - Flush Face Filler - Rip Return

** FTAB

LHS Reveal = 2	RHS Reveal = 2	Hor Reveal = 2
Top Reveal = 0	Bot Reveal = 0	
Toe Height = 0	Toe Recess = 50	
Left End =	Right End =	Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #3


Date: 22/10/26


Panel Stock

1	500	2100	Left End	33mm Laminex Terril Flint
1	520	2220	Right End	33mm Laminex Terril Flint
1	603.5	850	Unfinished Back LHS	18mm Laminex Terril Flint
1	482	2414	Top	33mm Laminex Terril Flint
1	482	2414	Bottom	33mm Laminex Terril Flint
1	1207	784	TV Back	18mm Laminex Terril Flint
1	603.5	850	Unfinished Back RHS	18mm Laminex Terril Flint
2	332	784	TV Back Cleat	16mm Carcase White Texture
2	200	784	TV Back Cleat	16mm Carcase White Texture
2	482	784	Partition	33mm Laminex Terril Flint
2	482	570.5	Fixed Shelf	33mm Laminex Terril Flint

Assembly #7 - Open Upper

2480 x 850 x 500 (1)

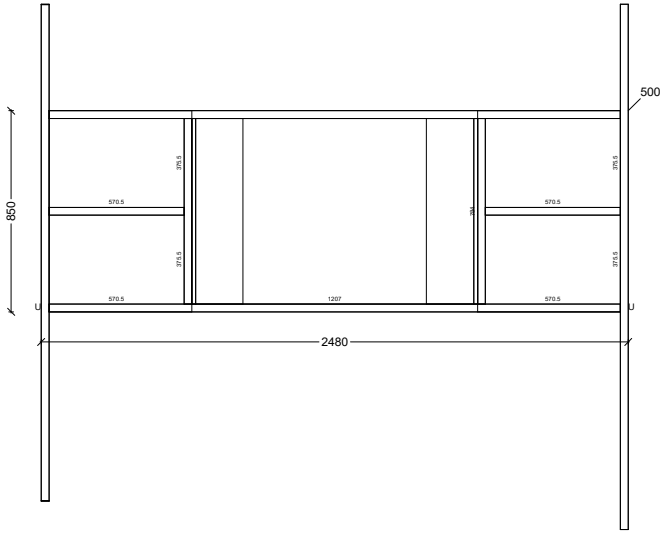



Assembly #7 - Open Upper

Ends Through Full height

LHS Reveal = 2	RHS Reveal = 2	Hor Reveal = 2
Top Reveal = 0	Bot Reveal = 0	
Toe Height = 0	Toe Recess = 50	
Left End = Unfinished	Right End = Unfinished	Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #3

Date: 22/10/26

Assembly #8 - Std Upper 2 Door

1207 x 450 x 480 (1)

Doors


2	601	448	Slab	18mm Laminex Terril Flint 1mr

Panel Stock


1	464	418	Left End	16mm Carcase White Texture
1	464	418	Right End	16mm Carcase White Texture
1	1207	418	Unfinished Back	16mm Carcase White Texture
1	480	1207	Top	16mm Carcase White Texture
1	480	1207	Bottom	16mm Carcase White Texture
1	454	1173	Adjustable Shelf	16mm Carcase White Texture

Hardware

2	Door Pull	Tip On	10
4	Hinge	Blum 110 Deg Hinge - Unsprung	47
4	Hinge Plate	Blum inline hinge plate 0mm	19.5

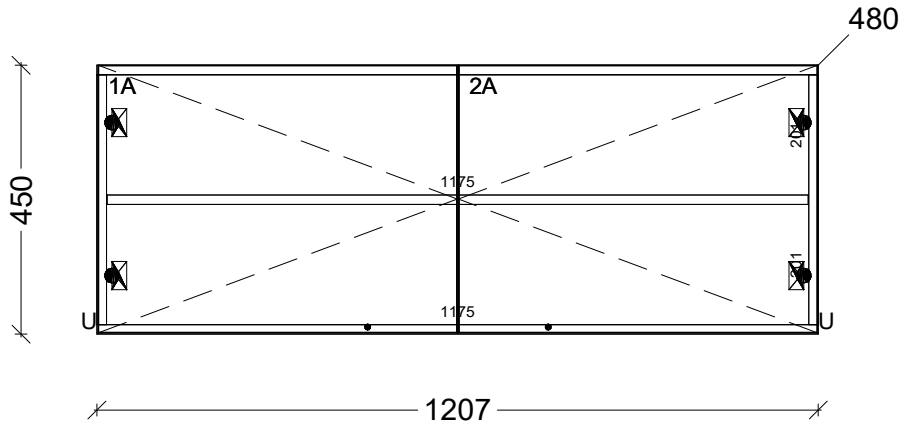

PUSH TO OPEN - USE UN-SPRUNG HINGES MOTHER FLIPPERS

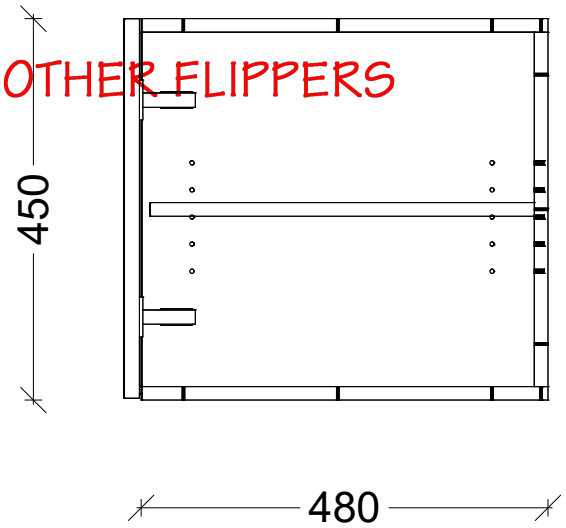

Assembly #8 - Std Upper 2 Door

** FTAB

LHS Reveal = 2 RHS Reveal = 1 Hor Reveal = 2

Top Reveal = 0 Bot Reveal = 2

Toe Height = 0 Toe Recess = 50

Left End = Unfinished Right End = Unfinished Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #3

Date: 22/10/26

Assembly #9 - Std Upper 2 Door

1207 x 450 x 480 (1)

Doors


2	601	448	Slab	18mm Laminex Terril Flint 1mr

Panel Stock


1	464	418	Left End	16mm Carcase White Texture
1	464	418	Right End	16mm Carcase White Texture
1	1207	418	Unfinished Back	16mm Carcase White Texture
1	480	1207	Top	16mm Carcase White Texture
1	480	1207	Bottom	16mm Carcase White Texture
1	454	1173	Adjustable Shelf	16mm Carcase White Texture

Hardware

2	Door Pull	Tip On	10
4	Hinge	Blum 110 Deg Hinge - Unsprung	47
4	Hinge Plate	Blum inline hinge plate 0mm	19.5

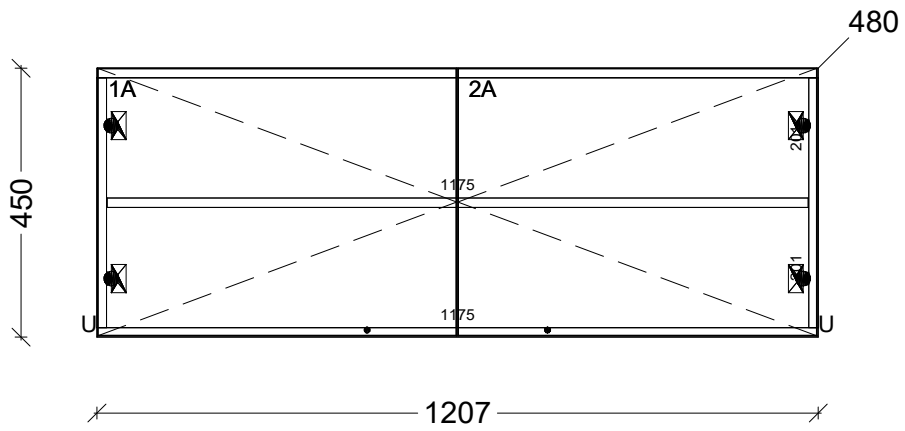

PUSH TO OPEN - USE UN-SPRUNG HINGES MOTHER FLIPPERS

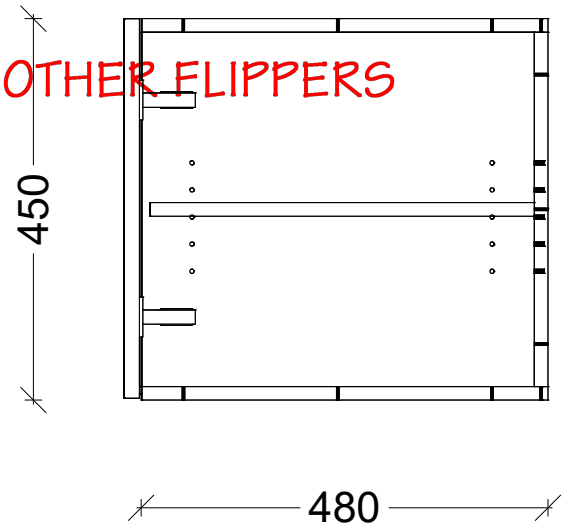

Assembly #9 - Std Upper 2 Door

** FTAB

LHS Reveal = 1 | RHS Reveal = 2 | Hor Reveal = 2

Top Reveal = 0 | Bot Reveal = 2

Toe Height = 0 | Toe Recess = 50

Left End = Unfinished | Right End = Unfinished | Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #3


Date: 22/10/26


Panel Stock

1	80	341.4	Sleeper	16mm Packing Sheet
2	80	341.4	Spreader	16mm Packing Sheet
1	100	300	Front Toe	16mm Packing Sheet
1	80	341.4	Sleeper	16mm Packing Sheet
1	100	300	Back Toe	16mm Packing Sheet
1	120	300	Skin - Front Toe	18mm Laminex Terril Flint
1	120	300	Skin - Back Toe	18mm Laminex Terril Flint

Assembly #10 - Toe Assembly

300 x 100 x 410 (1)

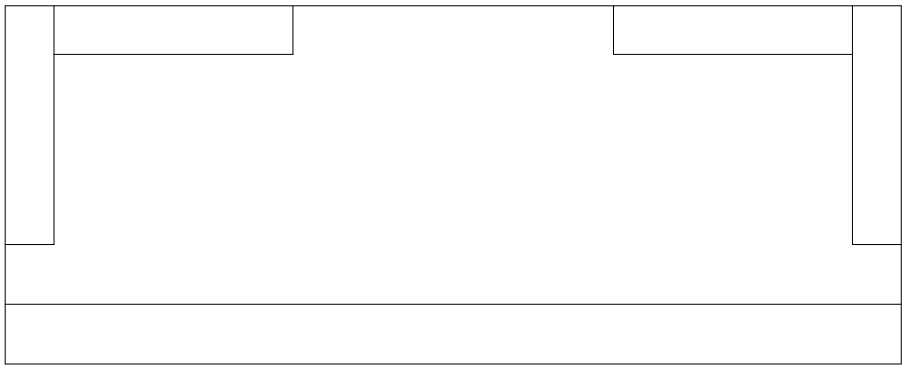

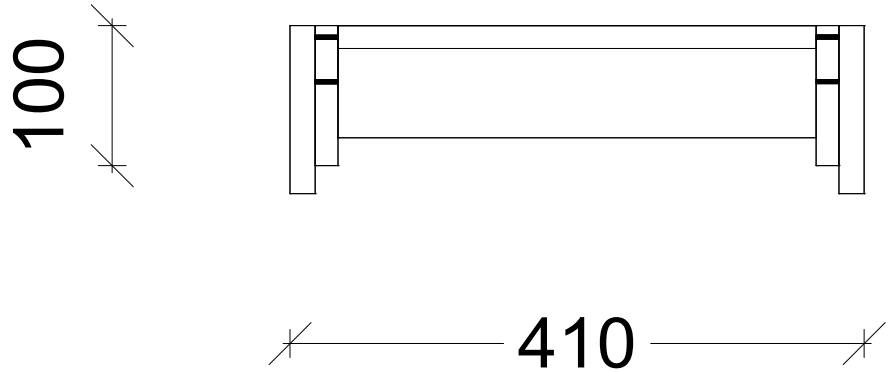

Assembly #10 - Toe Assembly

** FTAB

LHS Reveal = 2 | RHS Reveal = 2 | Hor Reveal = 2

Top Reveal = 3 | Bot Reveal = 0

Toe Height = 100 | Toe Recess = 18

Left End = Unfinished | Right End = Unfinished | Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #6


Date: 22/10/26

Panel Stock

1	1177	617	Panel	18mm Laminex Terril Flint

Assembly #11 - Modesty Panel

1177 x 617 x 18 (1)

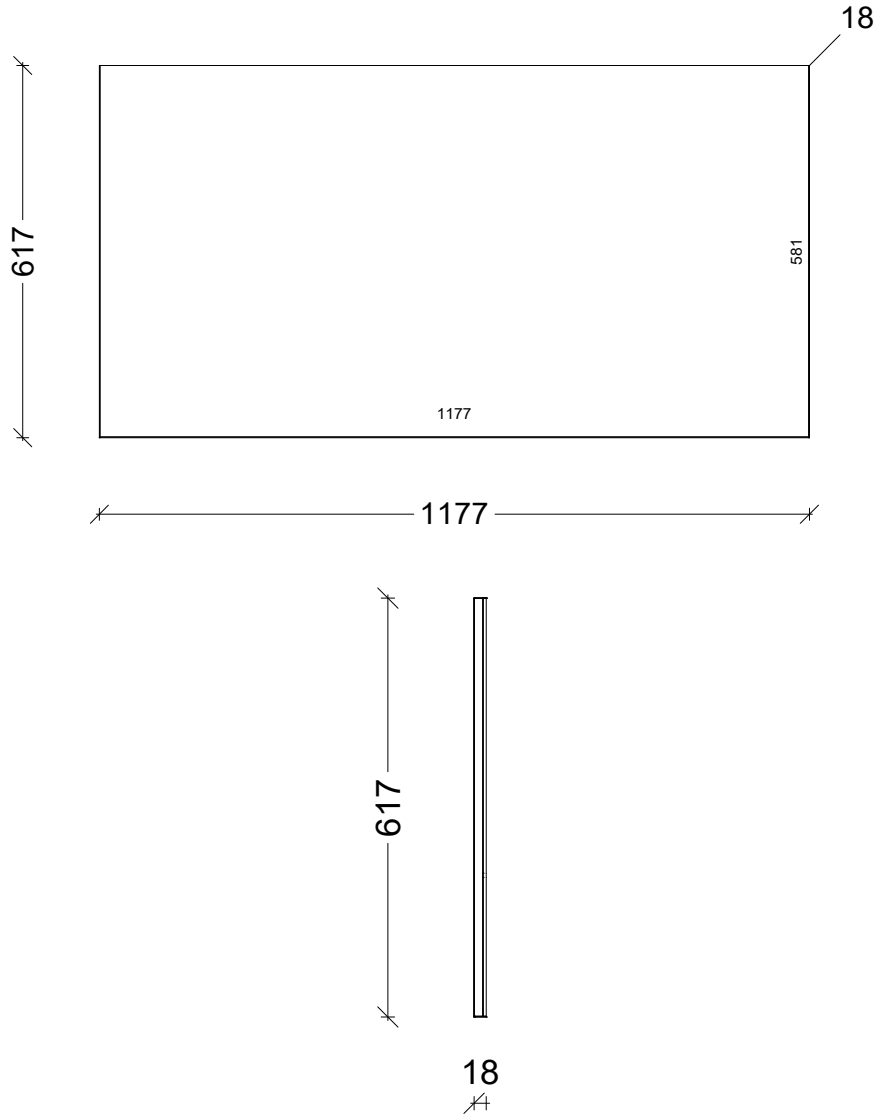

Assembly #11 - Modesty Panel

** FTAB

LHS Reveal = 2	RHS Reveal = 2	Hor Reveal = 2
Top Reveal = 3	Bot Reveal = 0	
Toe Height = 0	Toe Recess = 50	
Left End =	Right End =	Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #6


Date: 22/10/26

Panel Stock

1	480	737	Panel	18mm Laminex Terril Flint

Assembly #12 - Flush Base Panel to Floor

18 x 717 x 480 (1)

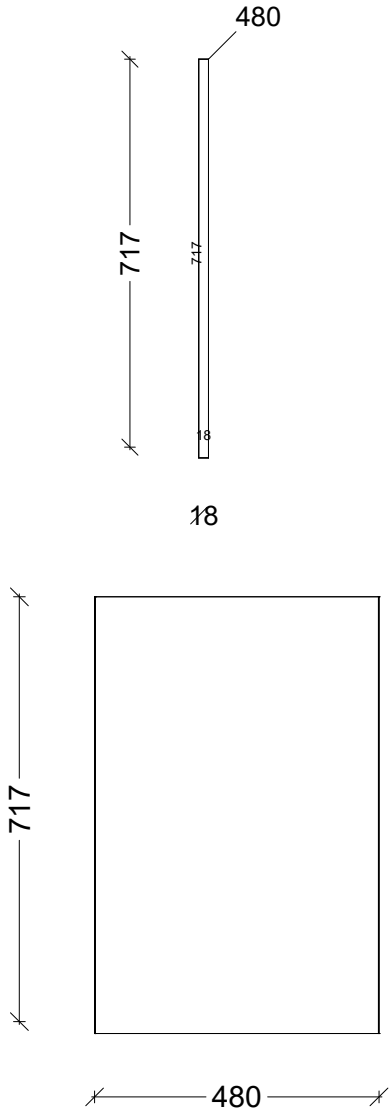

Assembly #12 - Flush Base Panel to Floor

** FTAB

LHS Reveal = 2	RHS Reveal = 2	Hor Reveal = 2
Top Reveal = 3	Bot Reveal = 0	
Toe Height = 0	Toe Recess = 50	
Left End =	Right End =	Back =

J1086 - Millers

Millers Transport Office

Office) - Wall #6

Date: 22/10/26

Drawer Fronts

2	296	306	Horizontal Grain	18mm Laminex Aged Walnut M

Panel Stock

1	444	585	Left End	16mm Carcase White Texture
1	444	585	Right End	16mm Carcase White Texture
1	300	585	Unfinished Back	16mm Carcase White Texture
1	460	300	Top	16mm Carcase White Texture
1	460	300	Bottom	16mm Carcase White Texture
1	233	390	Drawer Box Bottom 1	16mm Carcase White Texture
1	148	230	Drawer Box Back 1	16mm Carcase White Texture
1	233	390	Drawer Box Bottom 2	16mm Carcase White Texture
1	148	230	Drawer Box Back 2	16mm Carcase White Texture

Hardware

2	Drawer Pull	200mm Ferrara Black 160mm Centre	200
2 P	Drawer Guide	LBox Wte Bmn 40 Cx400	400

Notes


Drawer Annotation	DWR
Drawer 1 Depth	400
Drawer 2 Depth	400
Drawer 3 Depth	0
Drawer 1 Height	187.4
Drawer 1 Height	C
Drawer 2 Height	187.4
Drawer 3 Height	0
Drawer 2 Height	C
Drawer 3 Height	0.000000
Drawer 4 Depth	0
Drawer 4 Height	0
Drawer 4 Height	0.000000
Top Drawer Cutlery Error	0

Miscellaneous

4	Legrabox Bmn 40kg	370	LBox DG Bmn 40Kg 400
4	Legrabox Drw Side	400	LBox Side Wte C 400

Assembly #13 - 2 EQ Drawer Bank

300 x 617 x 460 (1)

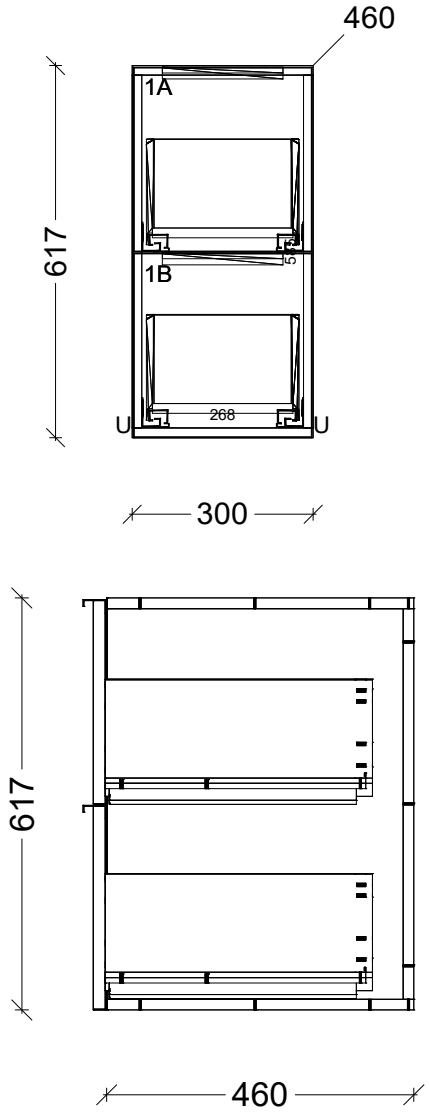

Assembly #13 - 2 EQ Drawer Bank

** FTAB

LHS Reveal = 2 RHS Reveal = 2 Hor Reveal = 2
Top Reveal = 3 Bot Reveal = 0
Toe Height = 0 Toe Recess = 50
Left End = Unfinished Right End = Unfinished Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #6

Date: 22/10/26

Miscellaneous

8	Legrabox Front Brkt	59.5	LBox Fnt Brkt M Exp
4	Legrabox Back Brkt	162.4	LBox Back Brkt Wte C

Assembly #13 - 2 EQ Drawer Bank

300 x 617 x 460 (1)

Assembly #13 - 2 EQ Drawer Bank

** FTAB

LHS Reveal = 2	RHS Reveal = 2	Hor Reveal = 2
Top Reveal = 3	Bot Reveal = 0	
Toe Height = 0	Toe Recess = 50	
Left End = Unfinished	Right End = Unfinished	Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #6


Date: 22/10/26

Panel Stock

1	480	737	Panel	18mm Laminex Terril Flint

Assembly #14 - Flush Base Panel to Floor

18 x 717 x 480 (1)

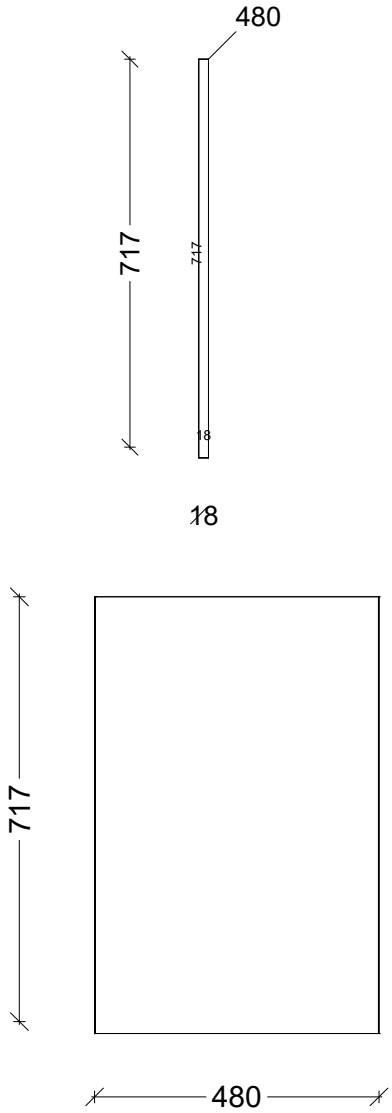

Assembly #14 - Flush Base Panel to Floor

** FTAB

LHS Reveal = 2	RHS Reveal = 2	Hor Reveal = 2
Top Reveal = 3	Bot Reveal = 0	
Toe Height = 0	Toe Recess = 50	
Left End =	Right End =	Back =

J1086 - Millers

Millers Transport Office

Office) - Wall #6


Date: 22/10/26


Panel Stock

1	400	737	Panel	33mm Laminex Aged Walnut M

Assembly #15 - Flush Base Panel to Floor

33 x 717 x 400 (1)

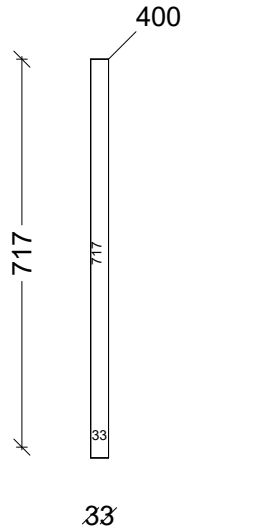

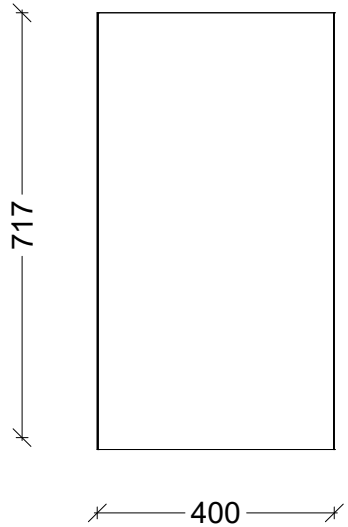

Assembly #15 - Flush Base Panel to Floor

** FTAB

LHS Reveal = 2	RHS Reveal = 2	Hor Reveal = 2
Top Reveal = 3	Bot Reveal = 0	
Toe Height = 0	Toe Recess = 50	
Left End =	Right End =	Back =

J1086 - Millers

Millers Transport Office

Office) - Wall #6


Date: 22/10/26


Panel Stock

1	47	421.4	Sleeper	16mm Packing Sheet
4	100	421.4	Spreader	16mm Packing Sheet
3	47	421.4	Sleeper	16mm Packing Sheet
1	67	1513.5	Front Toe	16mm Packing Sheet
1	67	1513.5	Back Toe	16mm Packing Sheet
1	87	1214	Skin - Front Toe	18mm Laminex Terril Flint
1	87	522	Skin - Left Toe	18mm Laminex Terril Flint
1	87	1562	Skin - Back Toe	18mm Laminex Terril Flint
1	87	68	Skin - Front Left Toe	18mm Laminex Terril Flint

Assembly #16 - Toe Assembly - Edged Not Mitred

1532 x 67 x 490 (1)



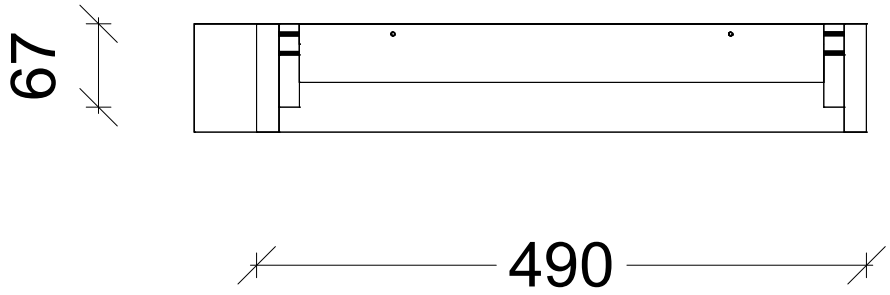

Assembly #16 - Toe Assembly - Edged Not Mitred

** FTAB

LHS Reveal = 2 | RHS Reveal = 2 | Hor Reveal = 2

Top Reveal = 3 | Bot Reveal = 0

Toe Height = 67 | Toe Recess = 18

Left End = Unfinished | Right End = Unfinished | Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #7


Date: 22/10/26


Panel Stock

1	1600	584	Back Panel	33mm Laminex Terril Flint
1	1600	590	Bottom	33mm Laminex Terril Flint
1	1600	590	Top	33mm Laminex Terril Flint
1	557	584	Left Panel	18mm Laminex Terril Flint
1	300	584	Left Blind Return	18mm Laminex Terril Flint
1	1600	584	DRAWING Back Panel	33mm Laminex Terril Flint

Assembly #17 - Island Panel to Floor

1582 x 584 x 33 (1)

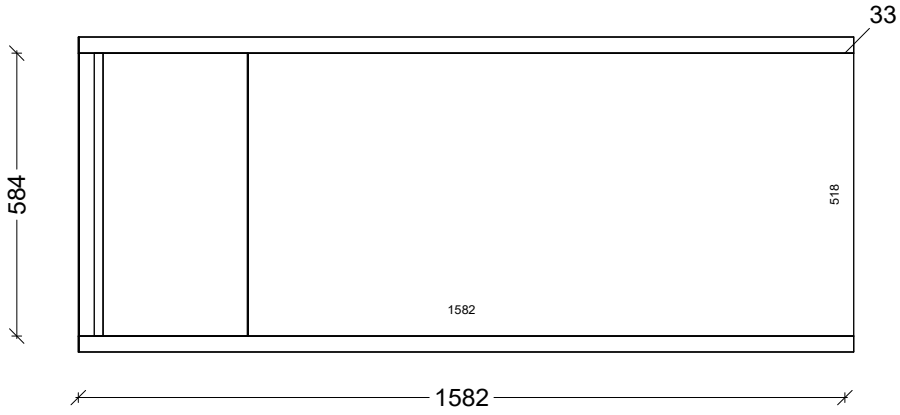

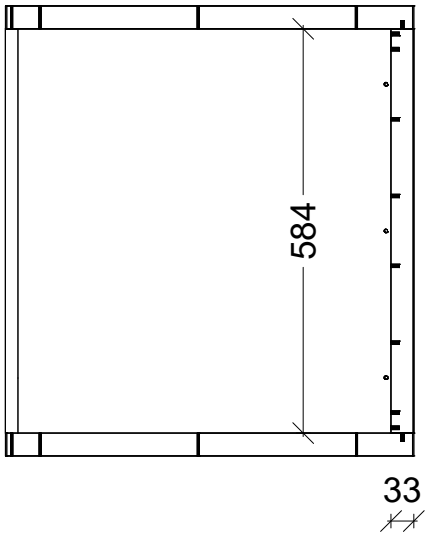

Assembly #17 - Island Panel to Floor

** FTAB

LHS Reveal = 2 | RHS Reveal = 2 | Hor Reveal = 2

Top Reveal = 3 | Bot Reveal = 0

Toe Height = 0 | Toe Recess = 50

Left End = | Right End = | Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #7


Date: 22/10/26

Panel Stock

1	537	584	Panel	18mm Laminex Terril Flint

Assembly #18 - Flush Base Panel to Kick

18 x 584 x 537 (1)

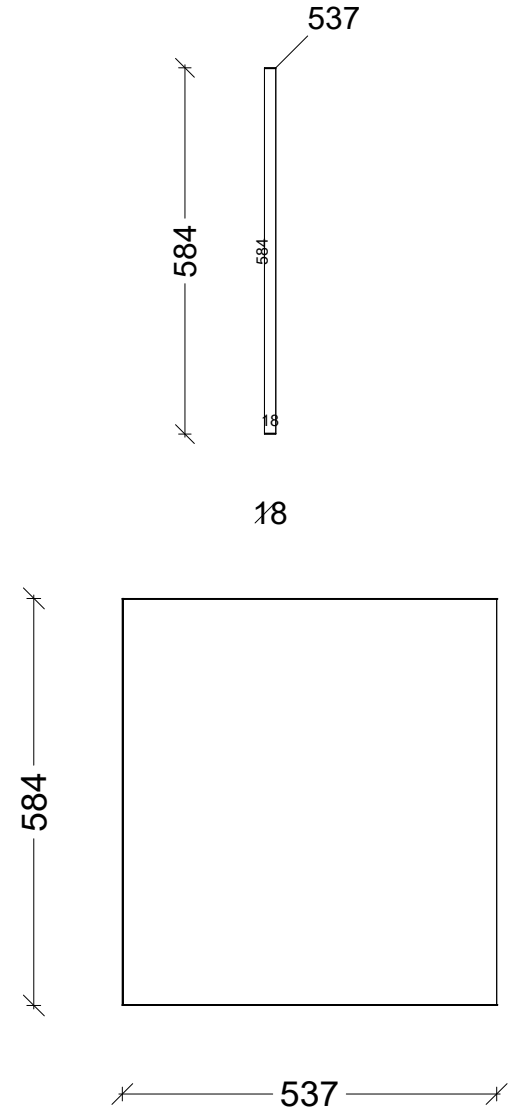

Assembly #18 - Flush Base Panel to Kick

** FTAB

LHS Reveal = 2	RHS Reveal = 1	Hor Reveal = 2
Top Reveal = 3	Bot Reveal = 0	
Toe Height = 0	Toe Recess = 50	
Left End =	Right End =	Back =

J1086 - Millers

Millers Transport Office

Office) - Wall #7

Date: 22/10/26

Drawer Fronts

2	316	289.5	Horizontal Grain	18mm Laminex Aged Walnut M

Panel Stock

1	521	552	Left End	16mm Carcase White Texture
1	521	552	Right End	16mm Carcase White Texture
1	300	552	Unfinished Back	16mm Carcase White Texture
1	537	300	Top	16mm Carcase White Texture
1	537	300	Bottom	16mm Carcase White Texture
1	233	490	Drawer Box Bottom 1	16mm Carcase White Texture
1	212	230	Drawer Box Back 1	16mm Carcase White Texture
1	233	490	Drawer Box Bottom 2	16mm Carcase White Texture
1	212	230	Drawer Box Back 2	16mm Carcase White Texture

Hardware

2	Drawer Pull	200mm Ferrara Black 160mm Centre	200
2 P	Drawer Guide	LBox Wte Bmn 40 Fx500	500

Notes


Drawer Annotation	DWR
Drawer 1 Depth	500
Drawer 2 Depth	500
Drawer 3 Depth	0
Drawer 1 Height	251.4
Drawer 1 Height	F
Drawer 2 Height	251.4
Drawer 3 Height	0
Drawer 2 Height	F
Drawer 3 Height	0.000000
Drawer 4 Depth	0
Drawer 4 Height	0
Drawer 4 Height	0.000000
Top Drawer Cutlery Error	0

Miscellaneous

4	Legrabox Bmn 40kg	370	LBox DG Bmn 40Kg 500
4	Legrabox Drw Side	500	LBox Side Wte F 500

Assembly #19 - 2 EQ Drawer Bank

300 x 584 x 537 (1)

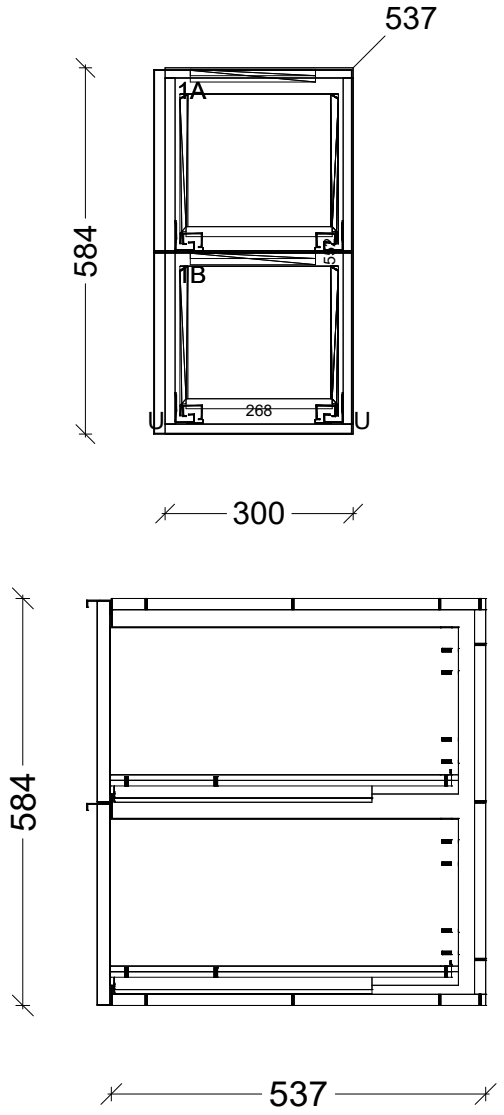

Assembly #19 - 2 EQ Drawer Bank

** FTAB

LHS Reveal = -18 | RHS Reveal = 2 | Hor Reveal = 2

Top Reveal = 3 | Bot Reveal = 0

Toe Height = 0 | Toe Recess = 50

Left End = Unfinished | Right End = Unfinished | Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #7

Date: 22/10/26

Miscellaneous

12	Legrabox Front Brkt	59.5	LBox Fnt Brkt M Exp
4	Legrabox Back Brkt	226.4	LBox Back Brkt Wte F

Assembly #19 - 2 EQ Drawer Bank

300 x 584 x 537 (1)

Assembly #19 - 2 EQ Drawer Bank

** FTAB

LHS Reveal = -18	RHS Reveal = 2	Hor Reveal = 2
Top Reveal = 3	Bot Reveal = 0	
Toe Height = 0	Toe Recess = 50	
Left End = Unfinished	Right End = Unfinished	Back = Unfinished

J1086 - Millers

Millers Transport Office

Office) - Wall #7


Date: 22/10/26

Panel Stock

1	60	584	Shadow Filler	18mm Laminex Terril Flint

Assembly #20 - Flush Filler to Kick

18 x 584 x 590 (1)

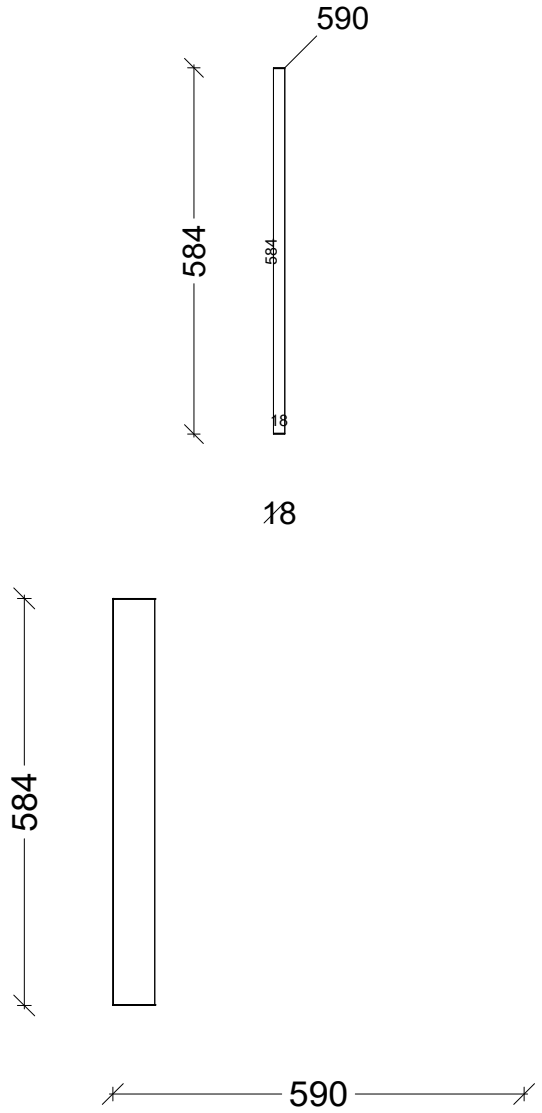

Assembly #20 - Flush Filler to Kick

** FTAB

LHS Reveal = 2	RHS Reveal = 2	Hor Reveal = 2
Top Reveal = 3	Bot Reveal = 0	
Toe Height = 0	Toe Recess = 50	
Left End =	Right End =	Back =

J1086 - Millers

Millers Transport Office

Office) - Wall #7

Date: 22/10/26
